MA: Sandwich - 180 Cotuit Road Performance report

2024

System Overview

Name: Sandwich - 180 Cotuit Road
Location: Sandwich, MA
Size AC: 3111 kWp
Size DC: 4357 kWp
Period: July 1, 2024 - Nov 30, 2024
Report Date: 12/10/24

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Sandwich - 180 Cotuit Road Performance

	Q1	Q2	Q3	Q4 (till Nov)	YTD
Actual Production MWH	429	635	821	352	2237
Expected Energy MWH*	248	665	579	214	1705
Estimated Production MWH**	1029	1741	1751	643	5163
Actual vs Expected	173%	96%	142%	164%	144%
Actual vs Estimated	42%	36%	47%	55%	45%

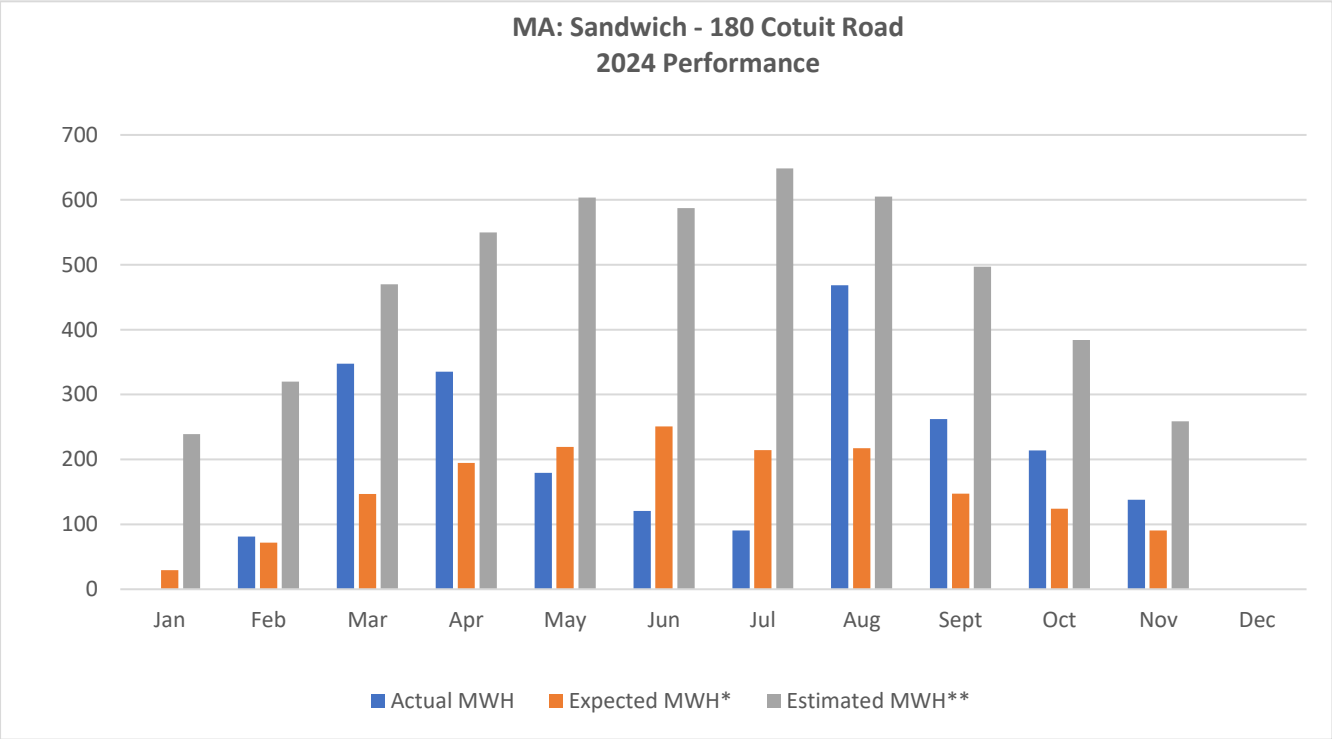

MA: Sandwich - 180 Cotuit Road Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Actual MWH	0	81	348	335	179	121	91	468	262	214	138	
Exp MWH*	29	72	147	194	219	251	214	217	147	124	90	
Est MWH**	239	320	470	550	604	587	648	605	497	384	259	
Act vs Exp	0%	113%	237%	172%	82%	48%	42%	216%	178%	172%	152%	
Act vs Est	0%	25%	74%	61%	30%	21%	14%	77%	53%	56%	53%	

Actual Performance in quarter 3 of 2024 was 173% of the Expected, Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 53%.

MA: Sandwich - 180 Cotuit Road July Production

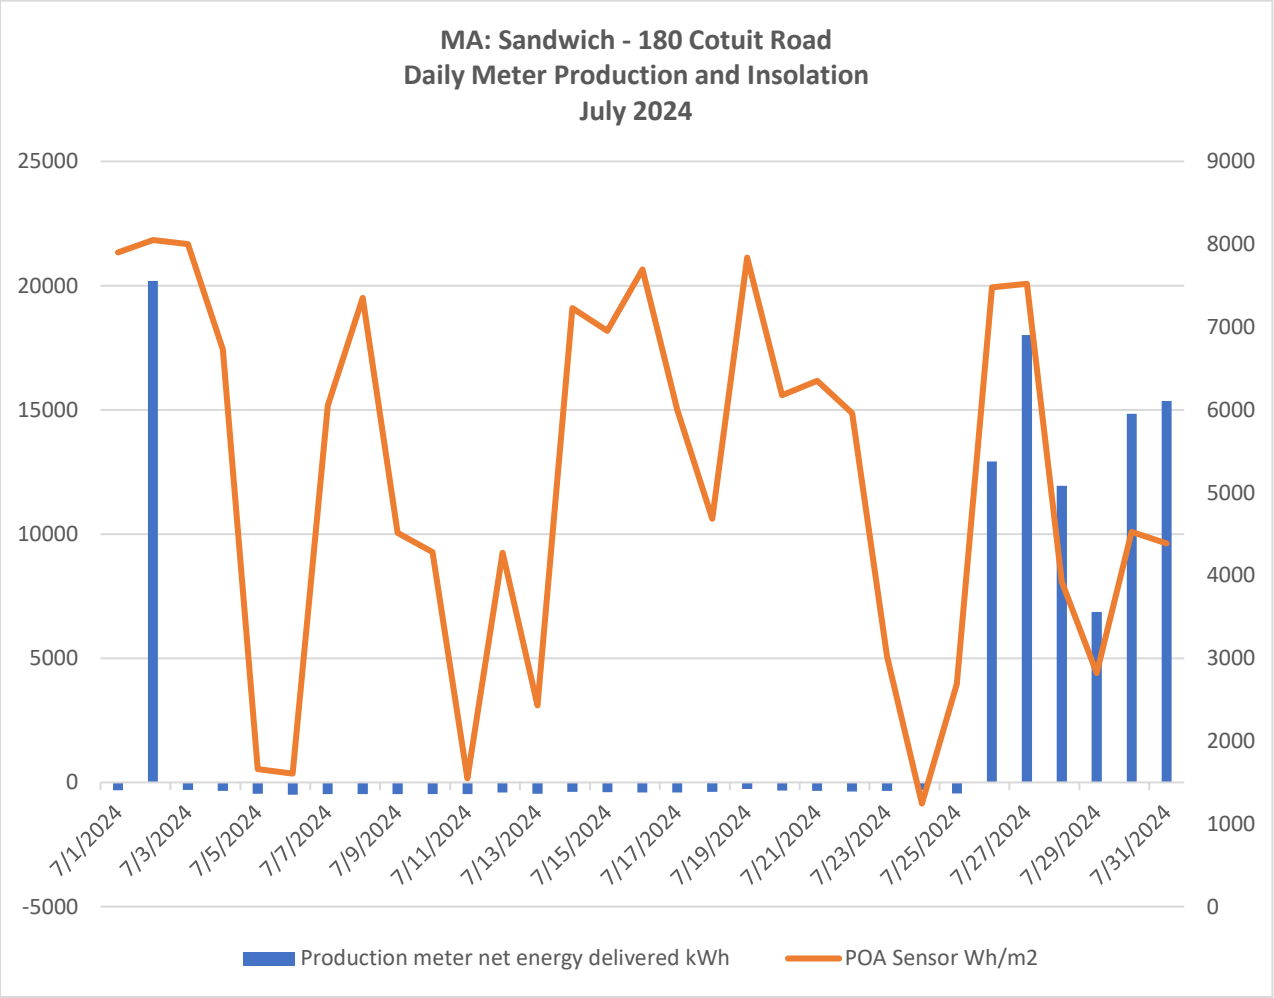

Events:-

1. Site was offline from 06/30 to 09:00am on 07/02 and again site was offline from 07/03 to 11:00am on 07/26. **SR088630**

MA: Sandwich - 180 Cotuit Road August Production

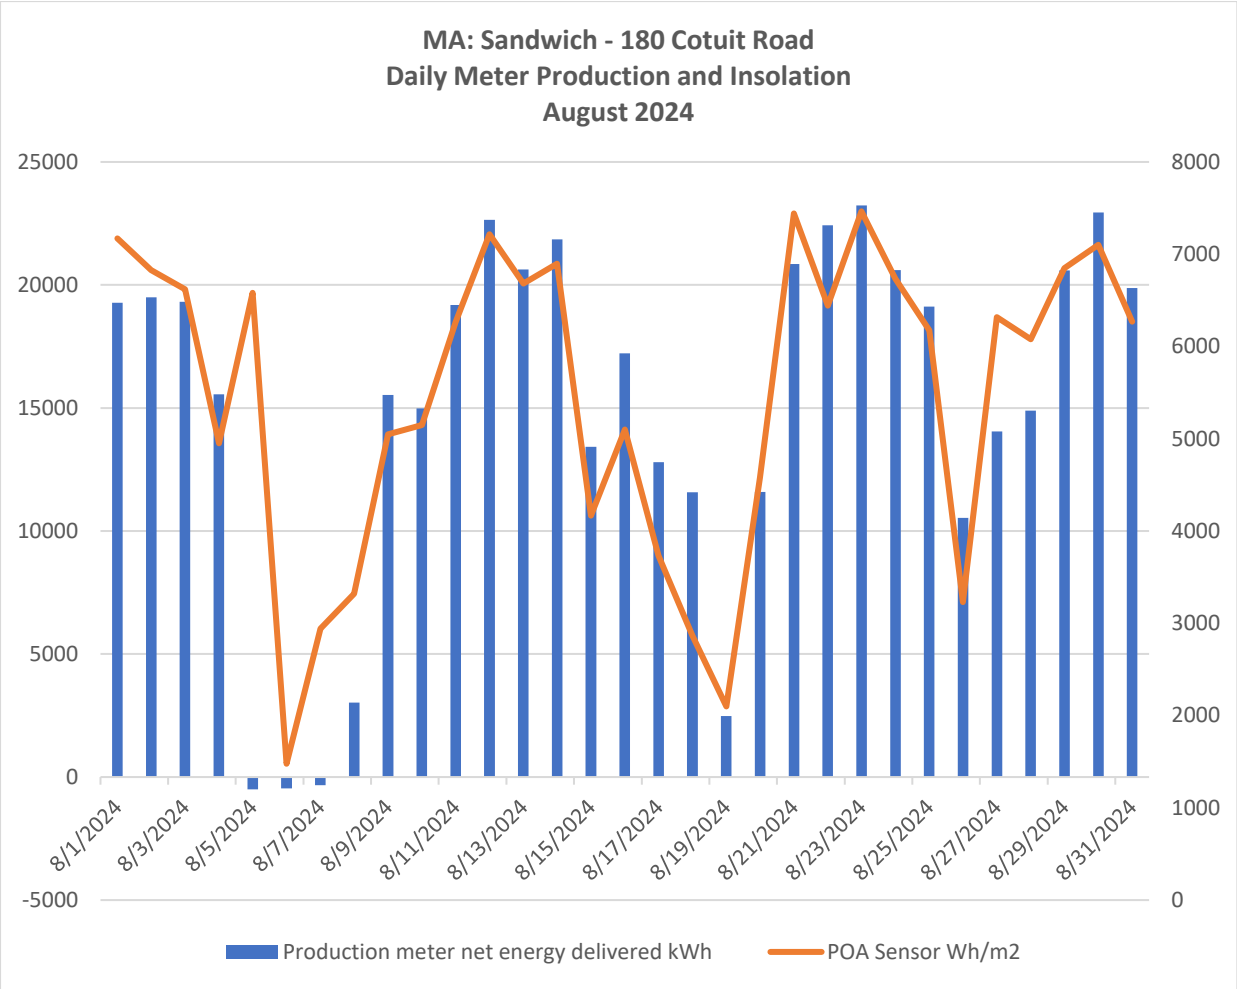

Events:-

1. Site offline from 5/8 and back online on 8/8 at 13:00. **SR088630**

2. Site offline from 07:00AM to 11:15AM on 8/20. **SR089286**

MA: Sandwich - 180 Cotuit Road September Production

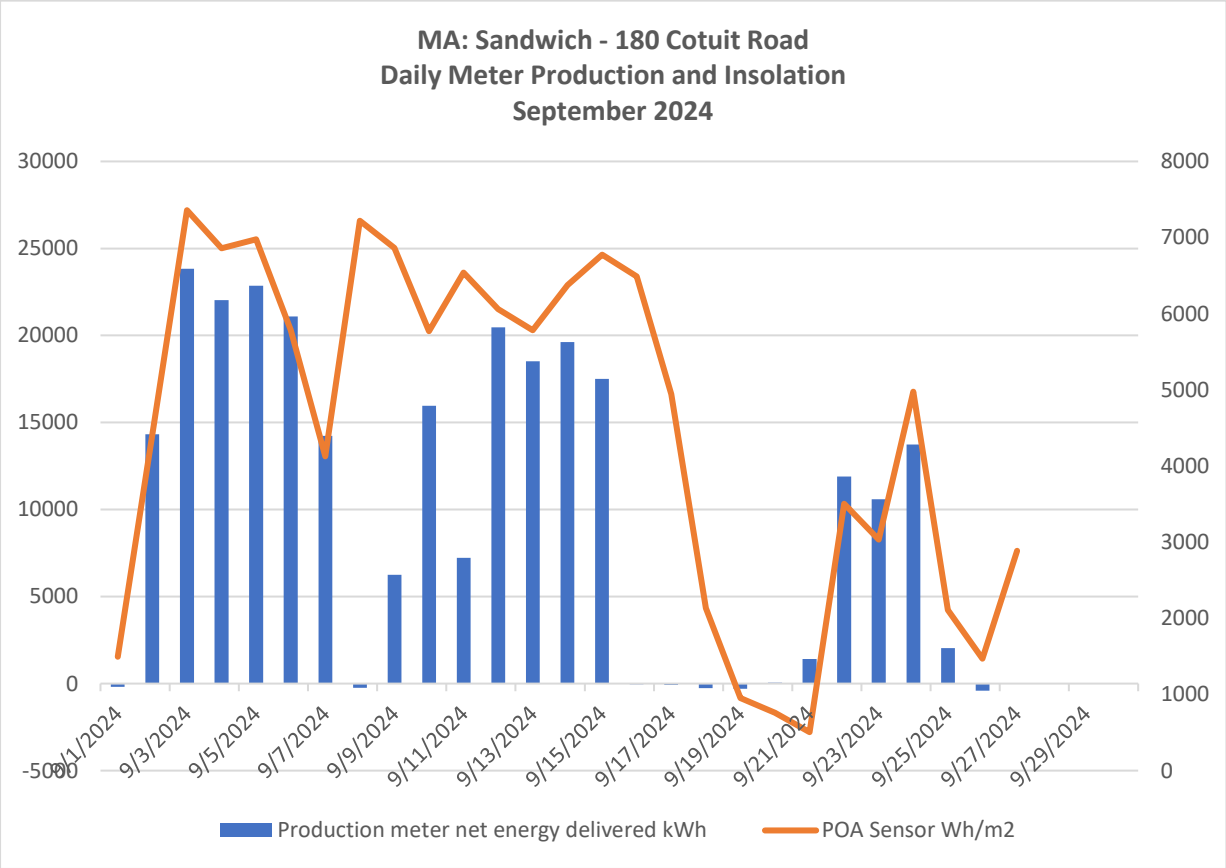

Events:-

1. Site tripped offline at 16:45 on 09/07 and back online at 12:30 on 09/09 and again tripped offline at 11:30 on 09/11 and back online at 08:30 on 09/12. **SR090185**

MA: Sandwich - 180 Cotuit Road October Production

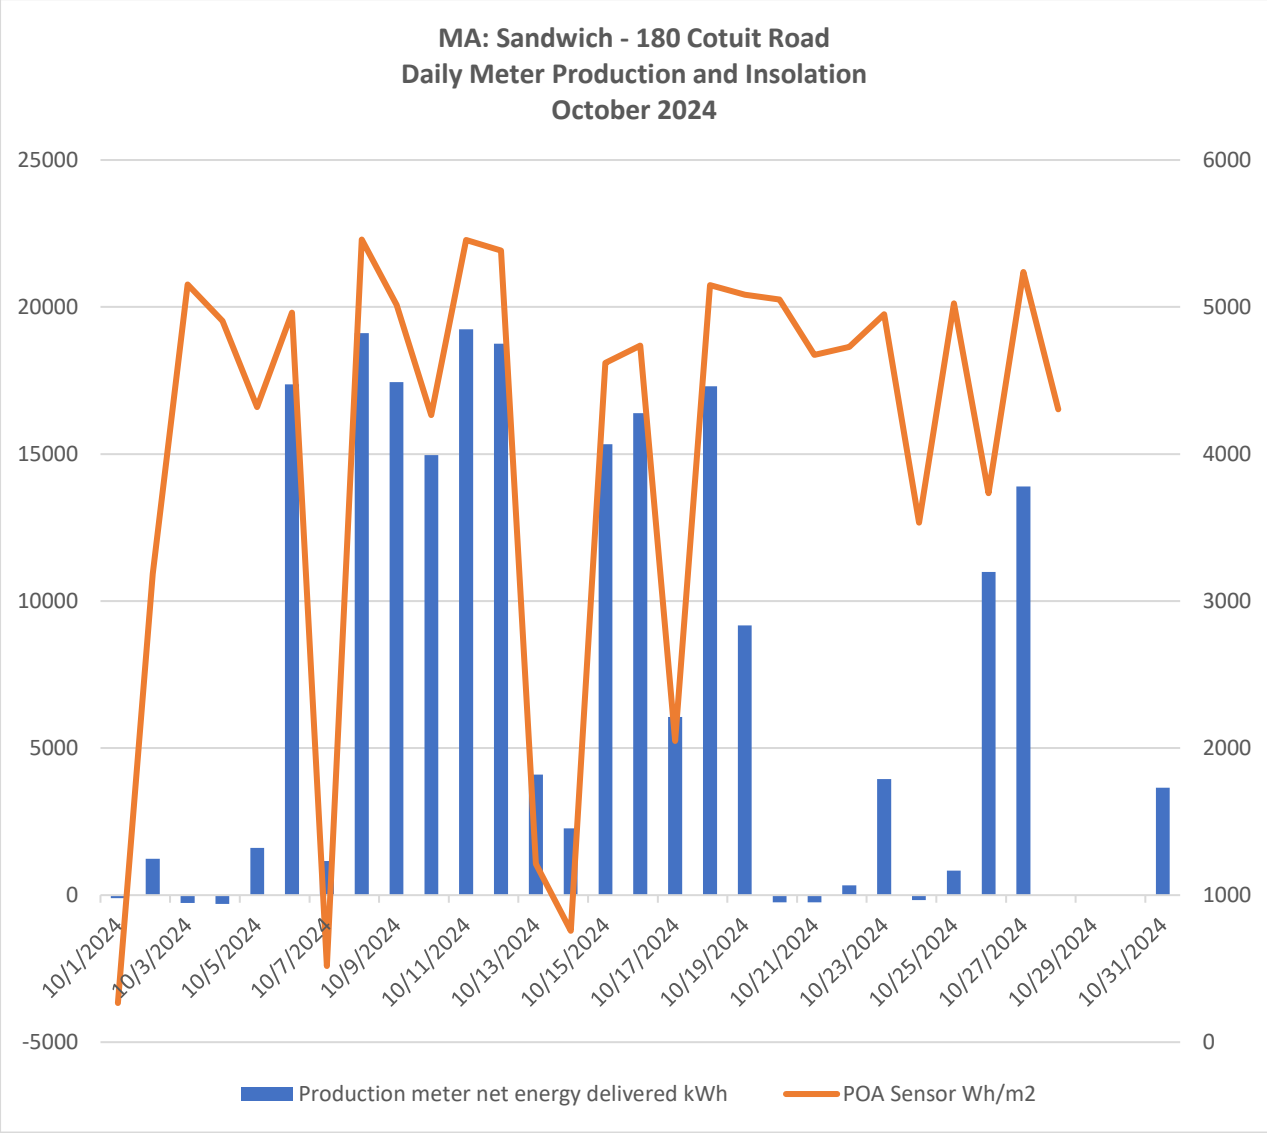

Events:-

1. Site was back online on 10/01 at 16:15. **SR091561**
2. Meter dropped to zero multiple days but voltages are available. **SR092515**
3. Site offline from 10/28 at 15:00 and. back online on 10/31 at 9:45 AM. **SR092623**

MA: Sandwich - 180 Cotuit Road November Production

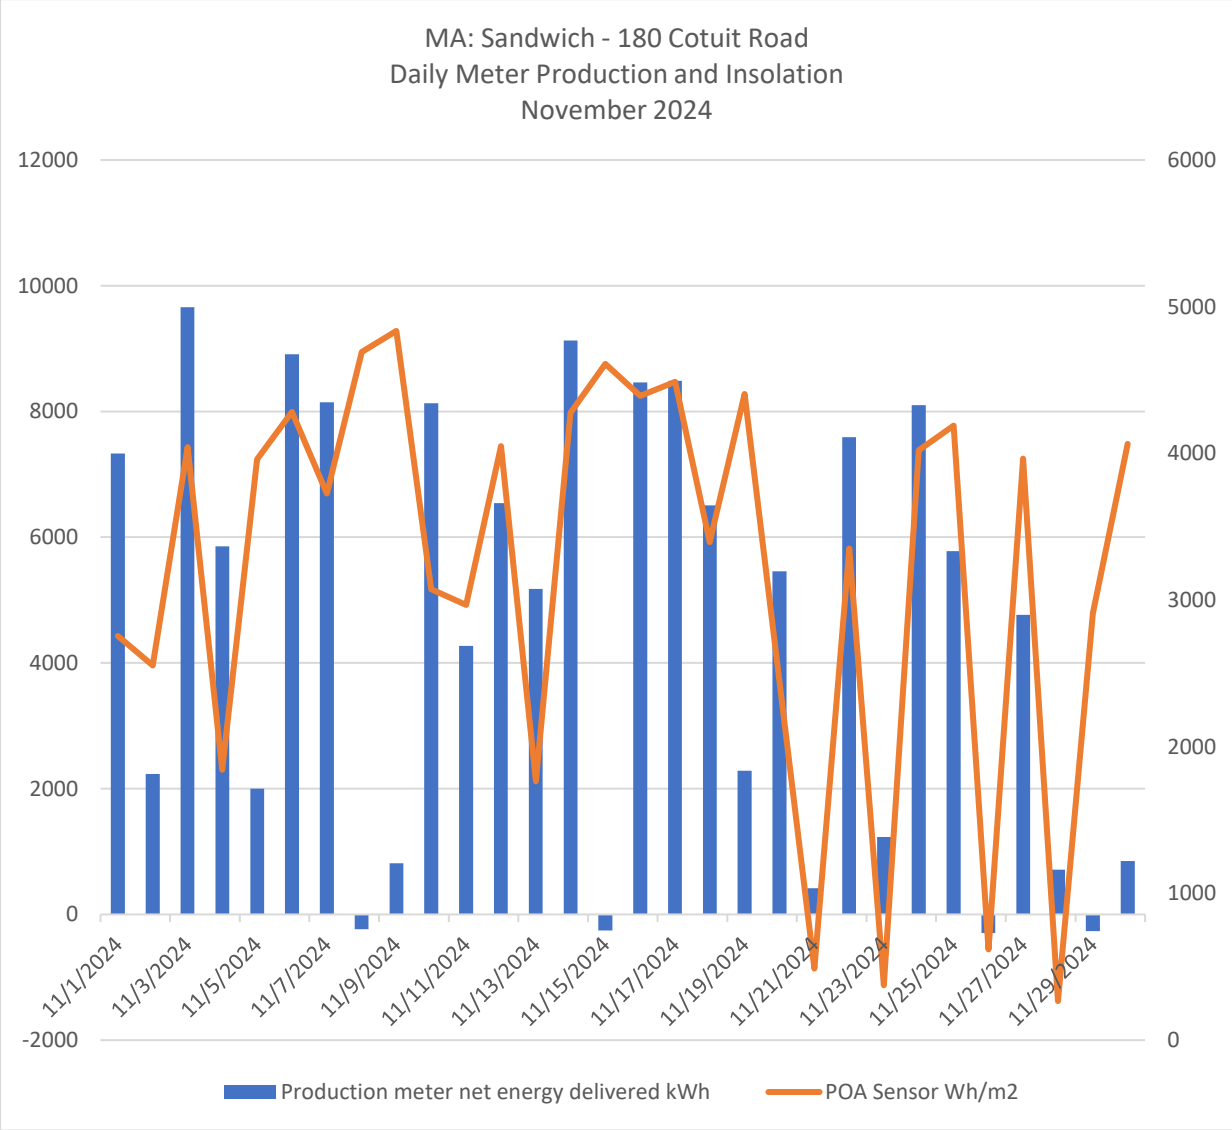

Events:-

1. The site tripped offline and later auto-reclosed on 11/01 at 11:00 PM, but the inverter remained offline. Ameresco dispatched a technician who restored inverter production on 11/02 at 1:00 PM. **SR092895**
2. Site tripped offline at 14:45 on 11/04 and back online at 12:30 on 11/05, again site was offline on 11/08 and back online at 13:30 on 11/09 and again site tripped offline at 12:45 on 11/11 and back online at 9:45 on 11/12 and was offline on 11/15 and back online on 11/16. **SR092950, SR093090 & SR093151**
3. Site tripped offline at 14:30 on 11/18 and back online at 12:15 on 11/19 and was offline on multiple days. **SR093377**

MA: Sandwich - 180 Cotuit Road Insolation

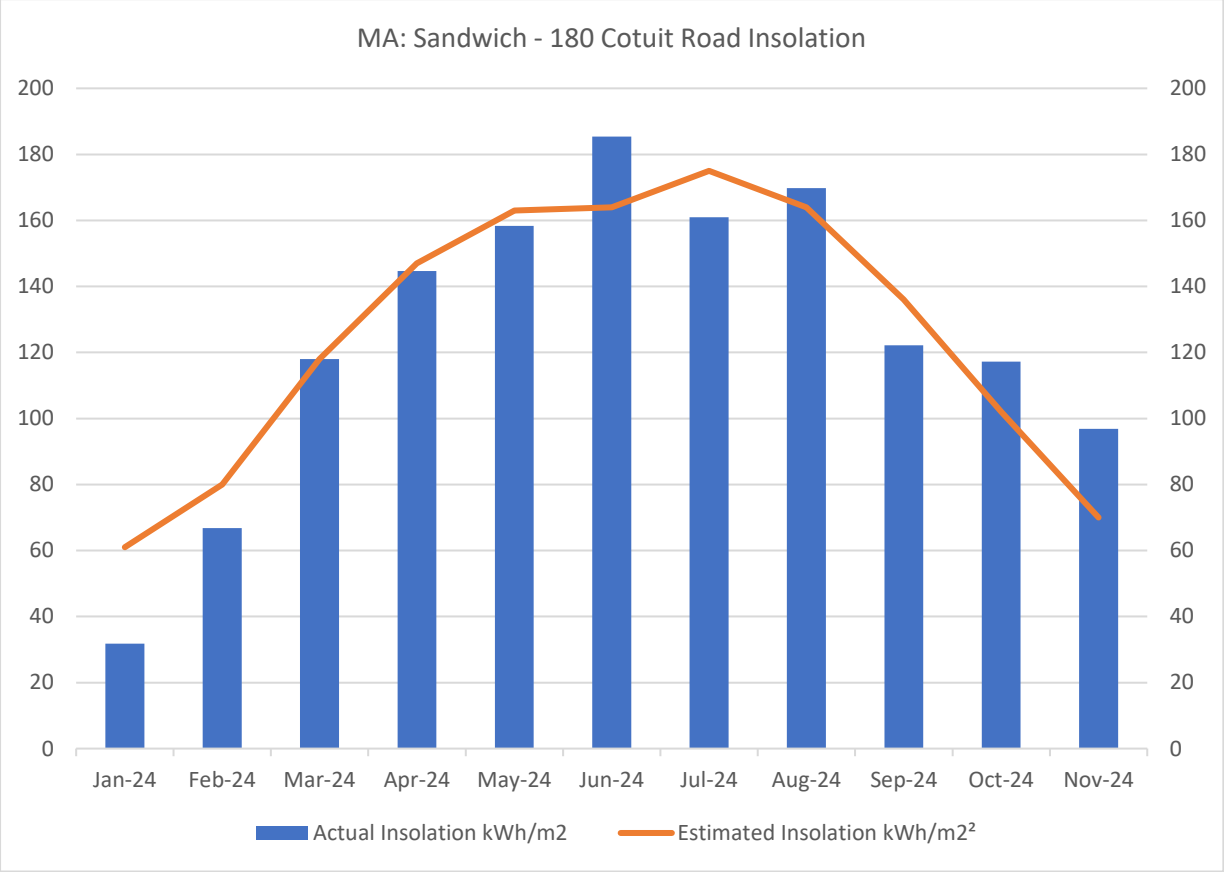

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec-24
Actual	32	67	118	145	158	185	161	170	122	117	97	
Estimated	61	80	118	147	163	164	175	164	136	102	70	
Act vs Est	52%	83%	100%	98%	97%	113%	92%	104%	90%	115%	138%	

Estimated Insolation = Also Energy Estimated Insolation
