MA: Sandwich - 180 Cotuit Road Performance report

2025

System Overview

Name: Sandwich - 180 Cotuit Road
Location: Sandwich, MA
Size AC: 3111 kWp
Size DC: 4357 kWp
Period: Jan 1, 2025 - Jan 31, 2025
Report Date: 02/12/25

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Sandwich - 180 Cotuit Road Performance

	Q1	Q2	Q3	Q4	YTD
Actual Production MWH	151				151
Expected Energy MWH*	104				104
Estimated Production MWH**	238				238
Actual vs Expected	146%				146%
Actual vs Estimated	63%				63%

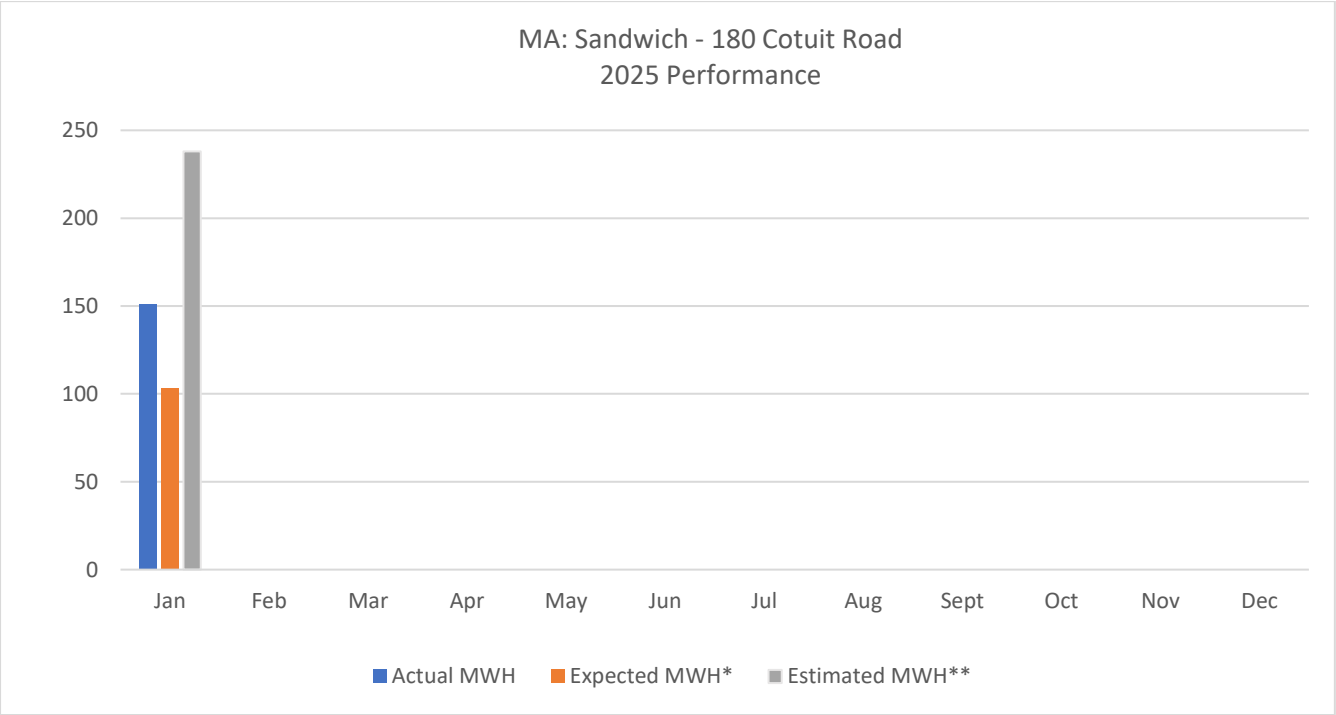

MA: Sandwich - 180 Cotuit Road Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Act MWH	151											
Exp MWH*	104											
Est MWH**	238											
Act vs Exp	146%											
Act vs Est	63%											

Actual Performance in January of 2025 was 146% of the Expected, Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 63%.

MA: Sandwich - 180 Cotuit Road January Production

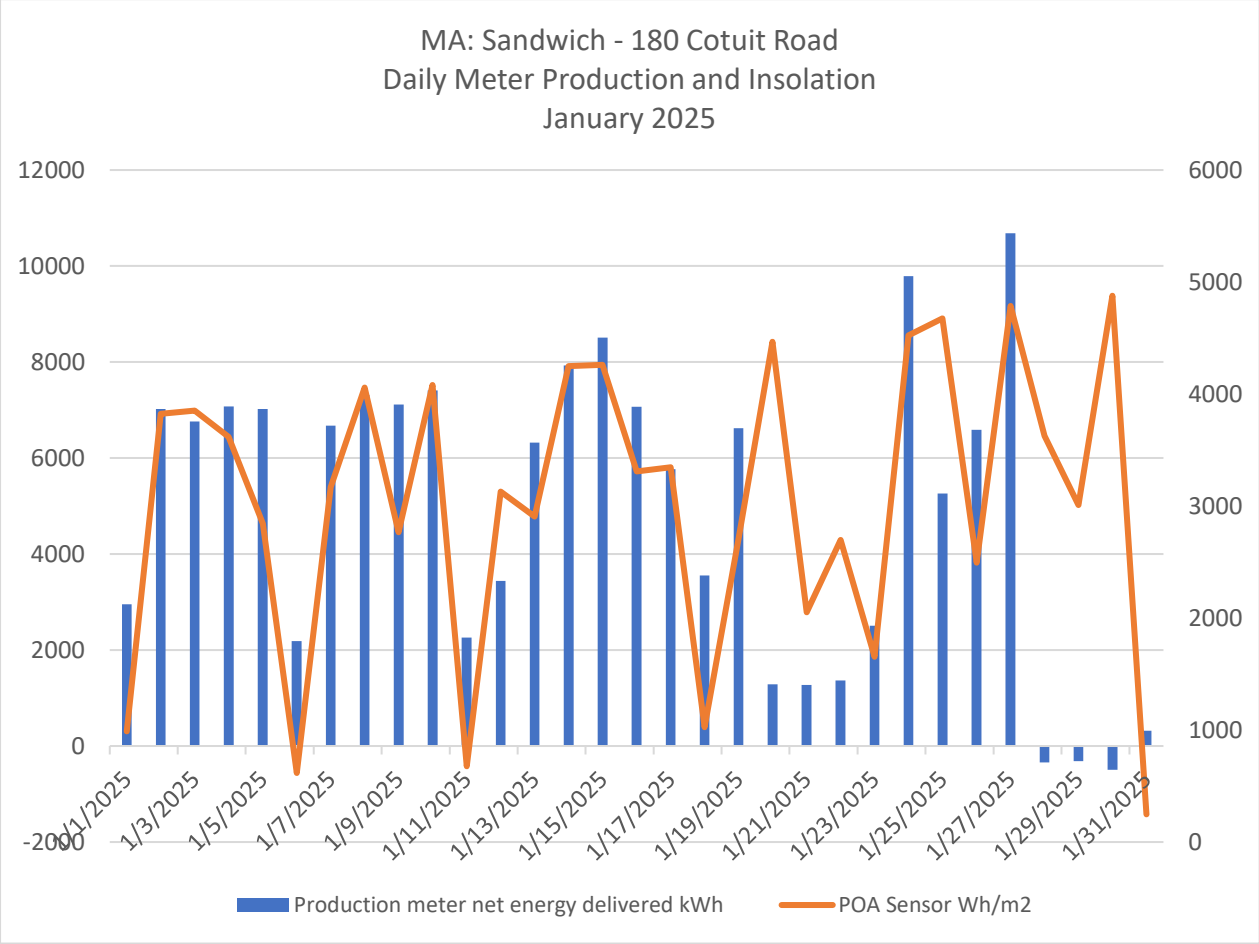

Events: -

1. The site was offline from 01/28 due to an inverter fault. Later, Power Electronics brought the site back online on 01/31 by pulling the logs. SR096048

MA: Sandwich - 180 Cotuit Road Insolation

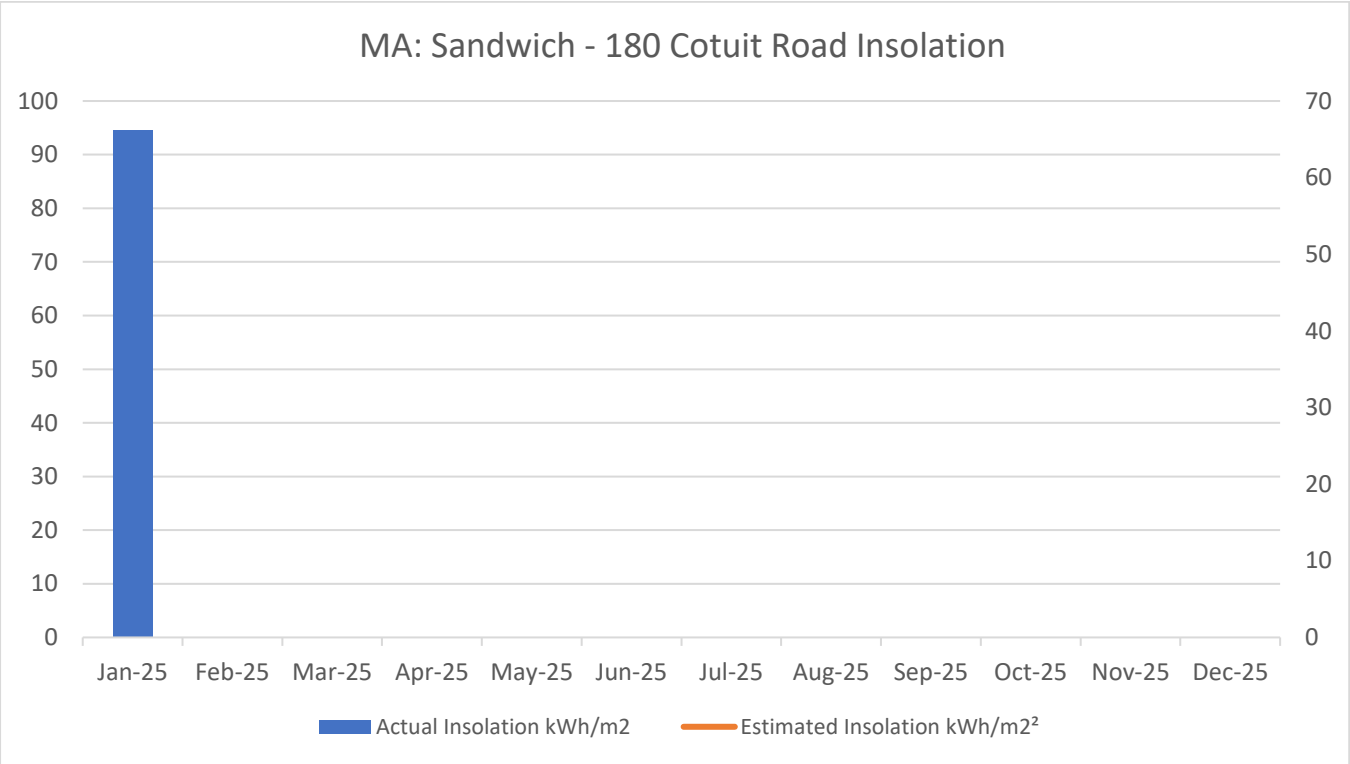

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Actual	95											
Estimated	58											
Act vs Est	162%											

Estimated Insolation = Also Energy Estimated Insolation
