MA: Sandwich - 180 Cotuit Road Performance report

Q1 2025

System Overview

Name: Sandwich - 180 Cotuit Road
Location: Sandwich, MA
Size AC: 3111 kW
Size DC: 4357 kWp
Period: Jan 1, 2025 – Mar 31, 2025
Report Date: 04/10/25

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Sandwich - 180 Cotuit Road Performance

	Q1	Q2	Q3	Q4	YTD
Actual Production MWH	796				796
Expected Energy MWH*	757				757
Estimated Production MWH**	1024				1024

Actual vs Expected	105%	105%
Actual vs Estimated	78%	78%

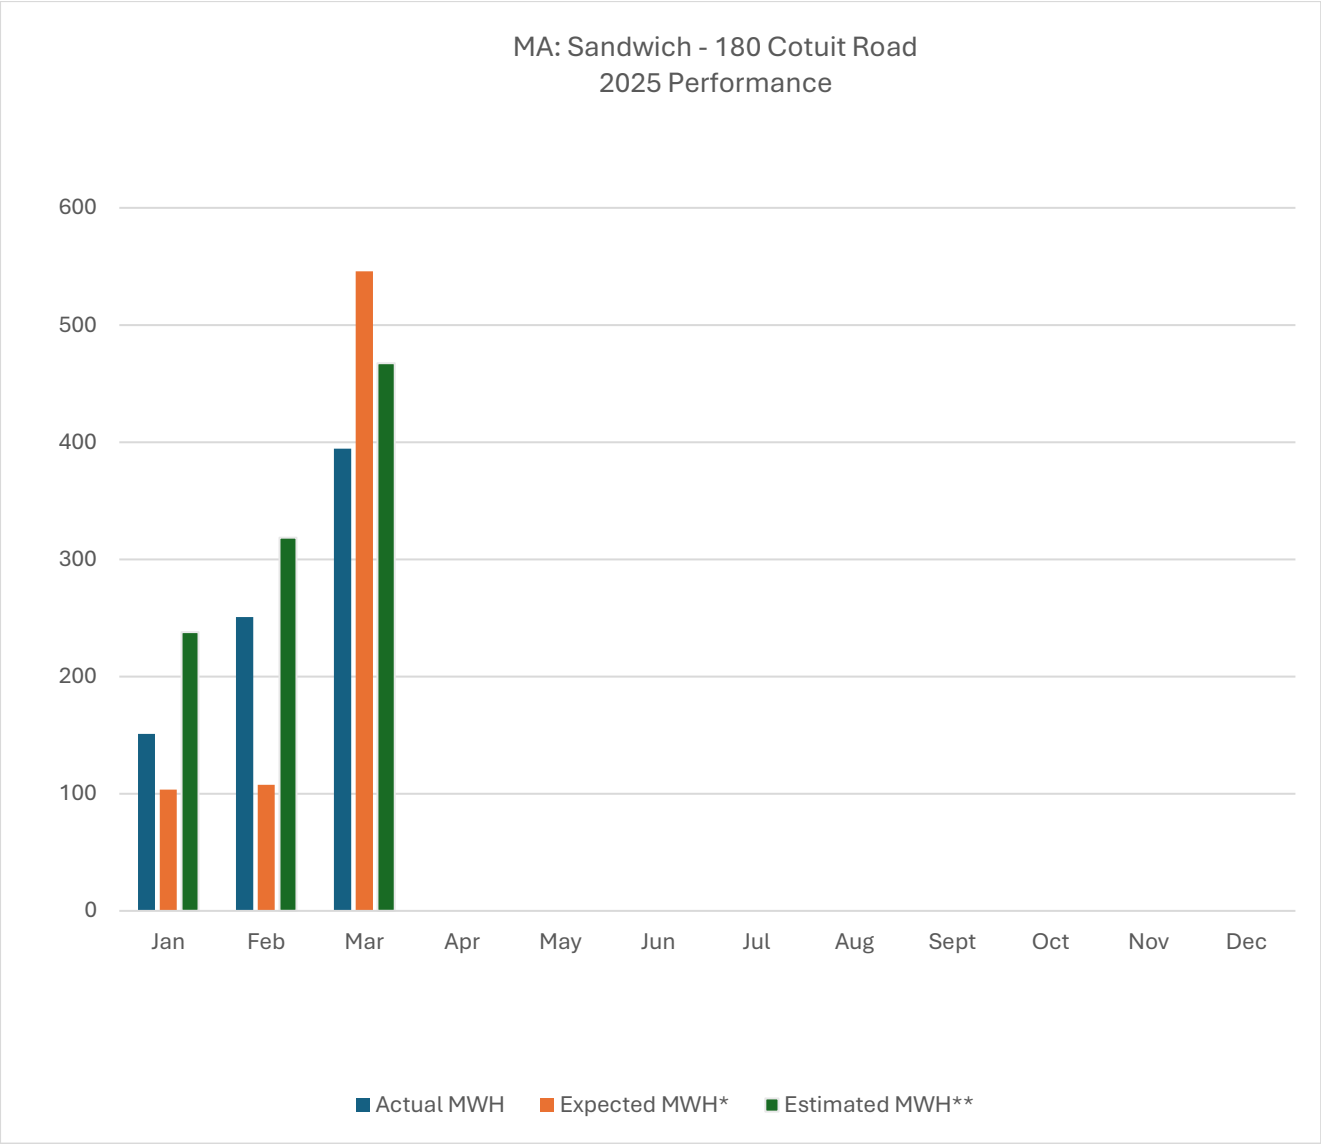

MA: Sandwich - 180 Cotuit Road Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Actual MWH	151	251	394									
Exp MWH*	104	108	546									
Est MWH**	238	318	467									
Act vs Exp	146%	233%	72%									
Act vs Est	63%	79%	84%									

Actual Performance in March 2025 was 72% of the Expected, Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 84%.

MA: Sandwich - 180 Cotuit Road January Production

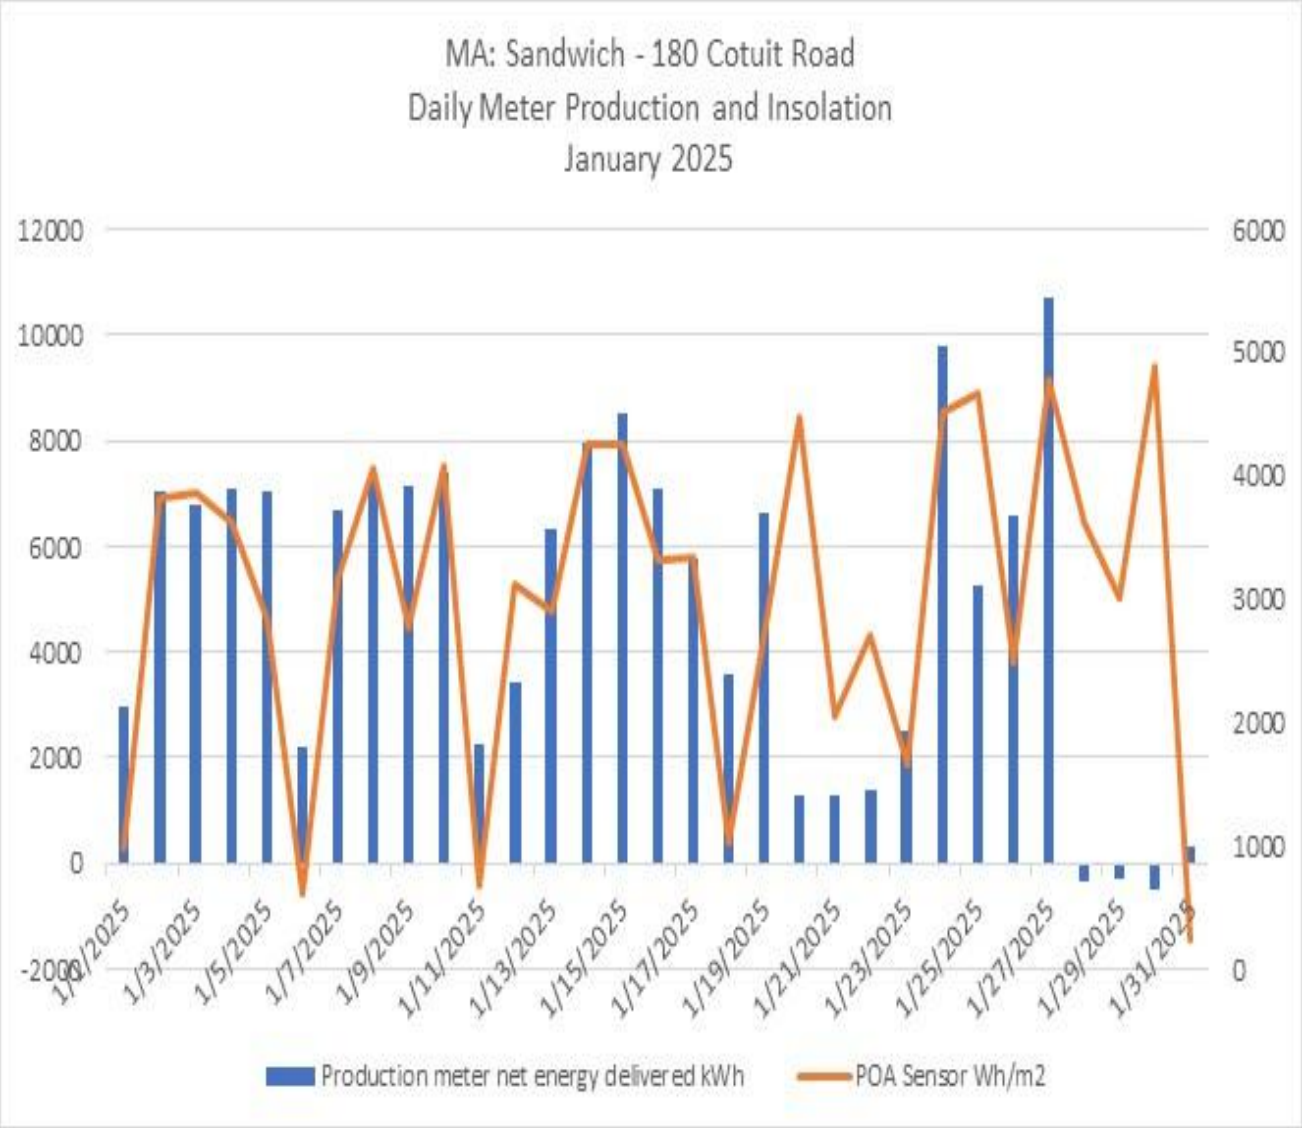

Events: -

1. The site was offline from 01/28 due to an inverter fault. Later, Power Electronics brought the site back online on 01/31 by pulling the logs. SR096048

MA: Sandwich - 180 Cotuit Road February Production

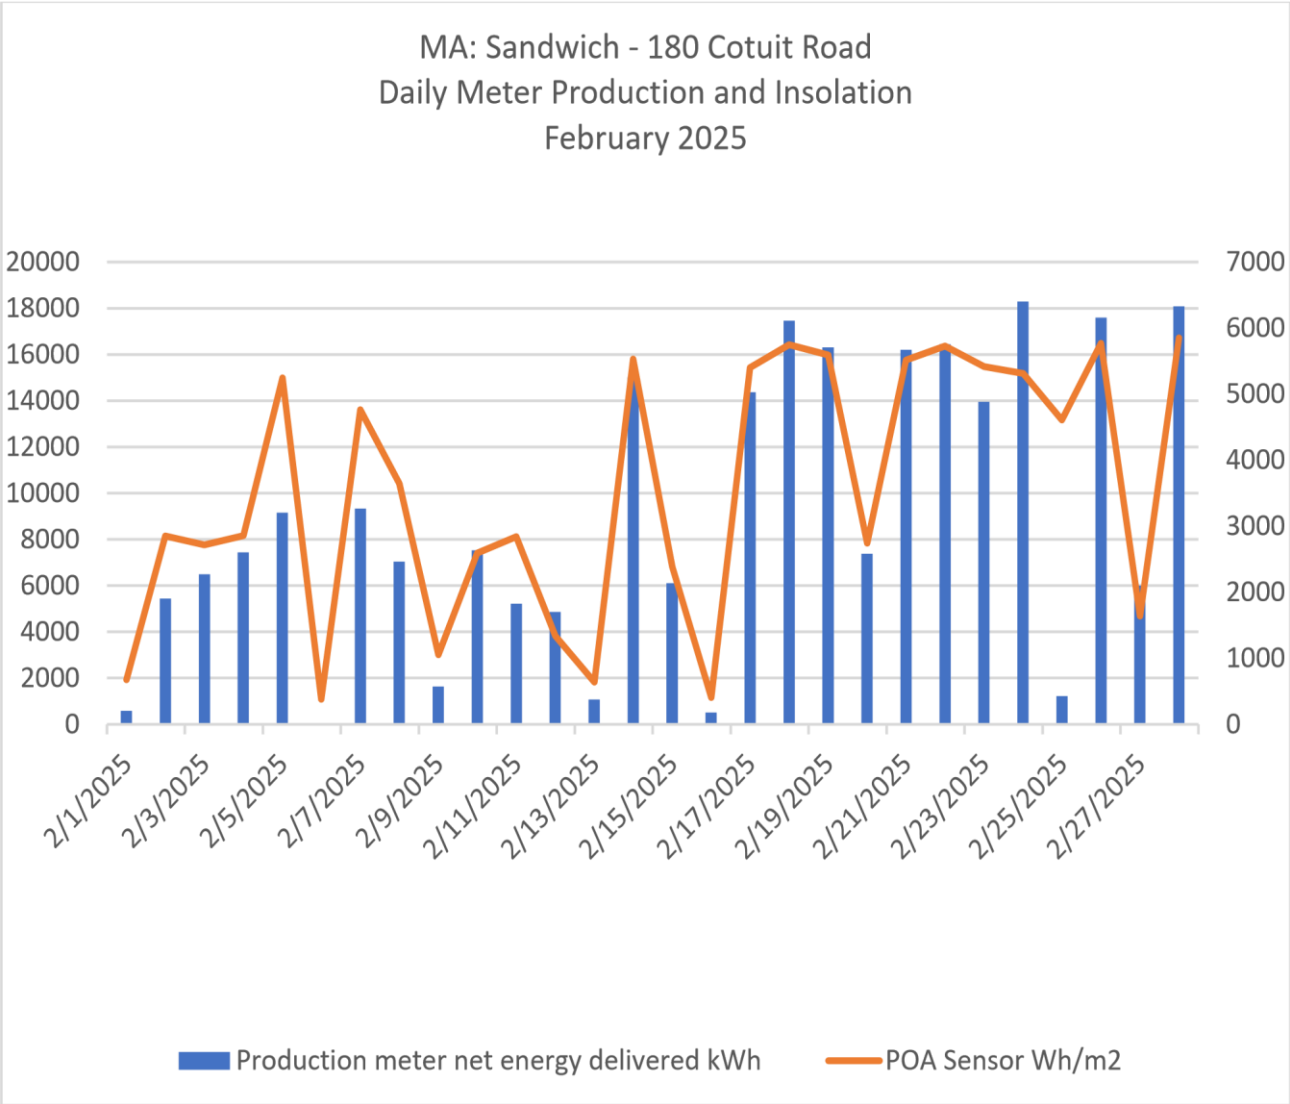

Events:

1. On 02/18/25, the technician found CB 15 strings 19 & 20 carrying 4 amps. Further investigation is needed to check for a ground fault or module issue. SR096077, SR097256.

2. The site was offline from 6:30 to 14:15 on 02/25/25 due to an inverter fault. The PE technician enabled all modules, put them in start mode, and brought the site back online. SR097746.

MA: Sandwich - 180 Cotuit Road March Production

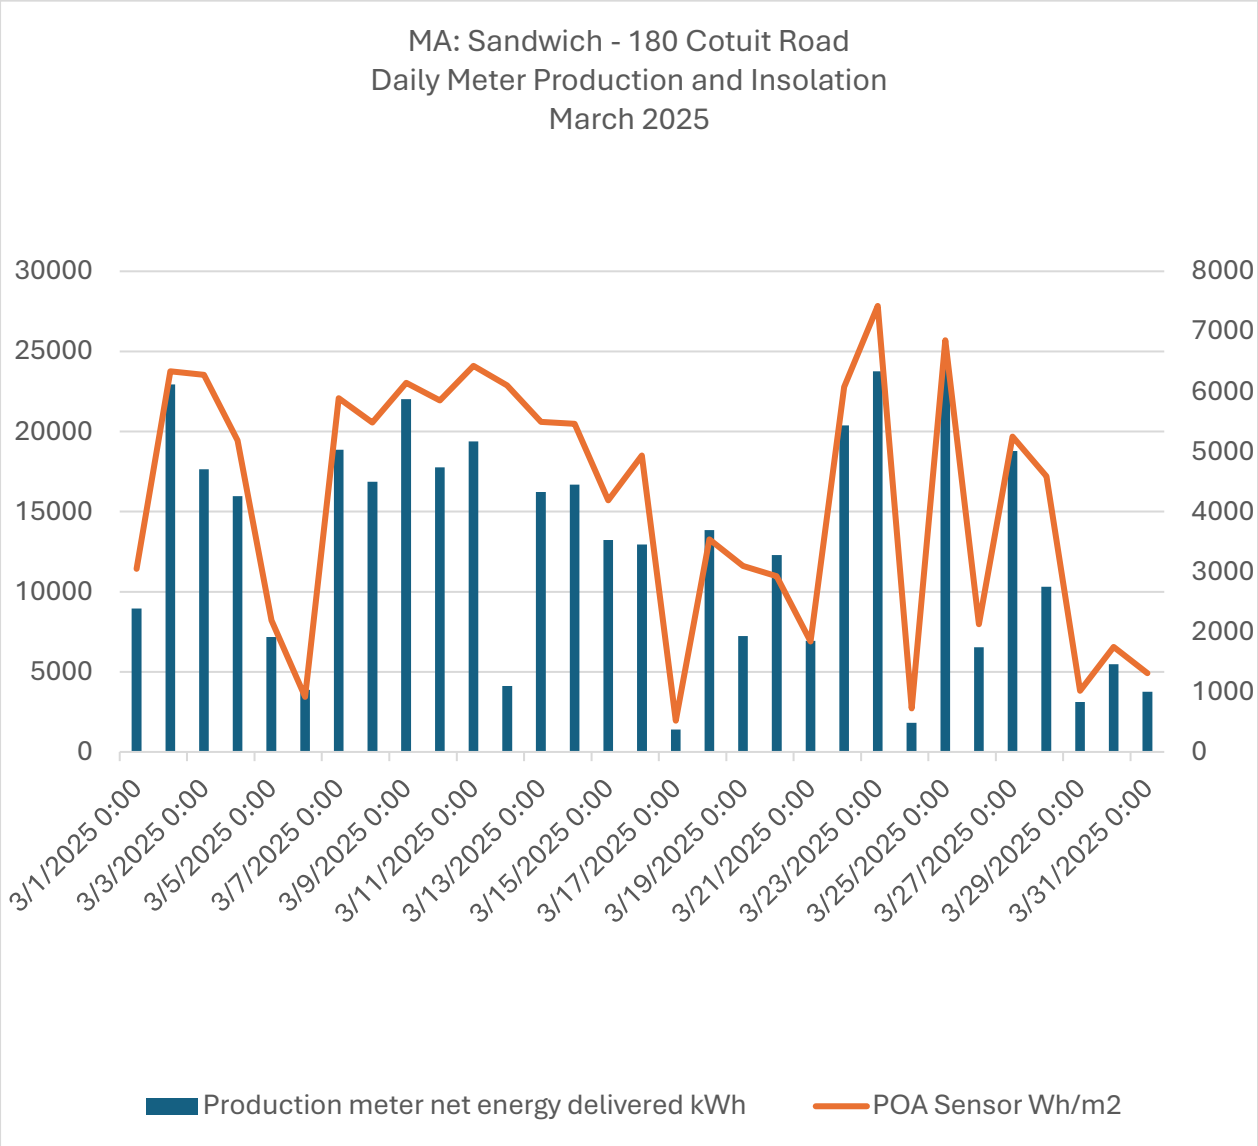

Events:

1. The site was taken offline from 08:30 to 14:45 on 03/12 due to an HVAC technician being on-site to check the site camera. SR098449
2. Power Electronics on site to perform retrospective ventilation. The Inverter will be taken offline from 11:30 to 13:15 on 03/28. SR099079
3. On 02/18/25, the technician found CB 15 strings 19 & 20 carrying 4 amps. Further investigation is needed to check for a ground fault or module issue. SR096077, SR097256, SR099474

MA: Sandwich - 180 Cotuit Road Insolation

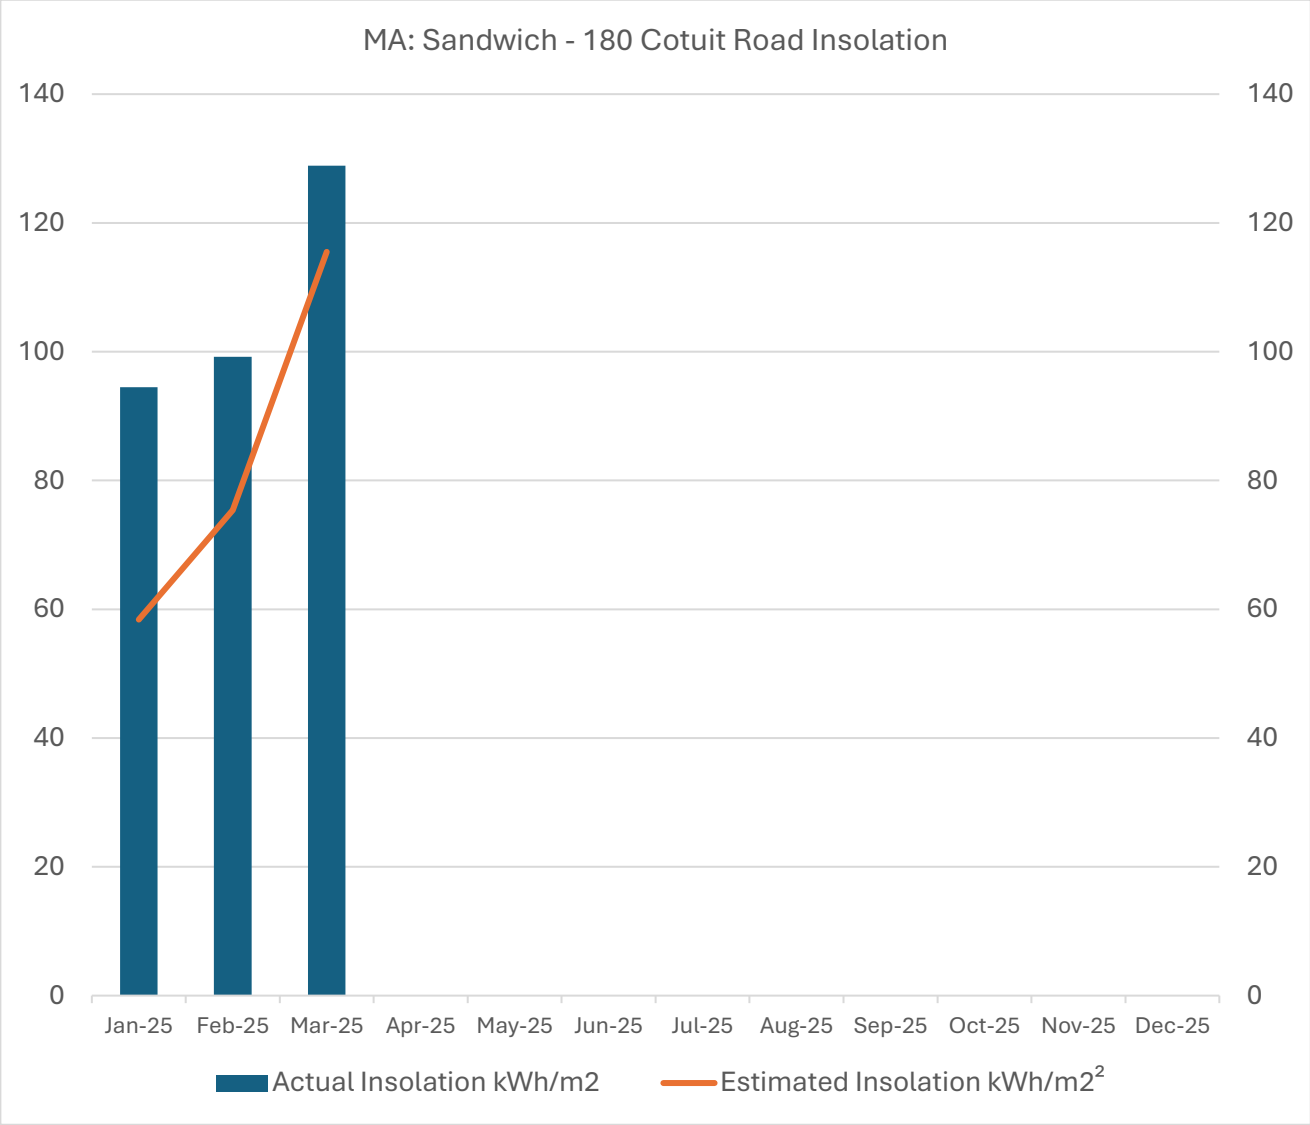

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Actual	95	99	129									
Est	58	75	115.5									
Act vs Est	162%	132%	112%									

Estimated Insolation = Also Energy Estimated Insolation
