MA: Sandwich - 180 Cotuit Road Performance report

2025

System Overview

Name: Sandwich - 180 Cotuit Road
Location: Sandwich, MA
Size AC: 3111 kWp
Size DC: 4357 kWp
Period: Feb 1, 2025 - Feb 28, 2025
Report Date: 03/11/25

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Sandwich - 180 Cotuit Road Performance

	Q1	Q2	Q3	Q4	YTD
Actual Production MWH	402				402
Expected Energy MWH*	211				211
Estimated Production MWH**	556				556
Actual vs Expected	190%				190%
Actual vs Estimated	72%				72%

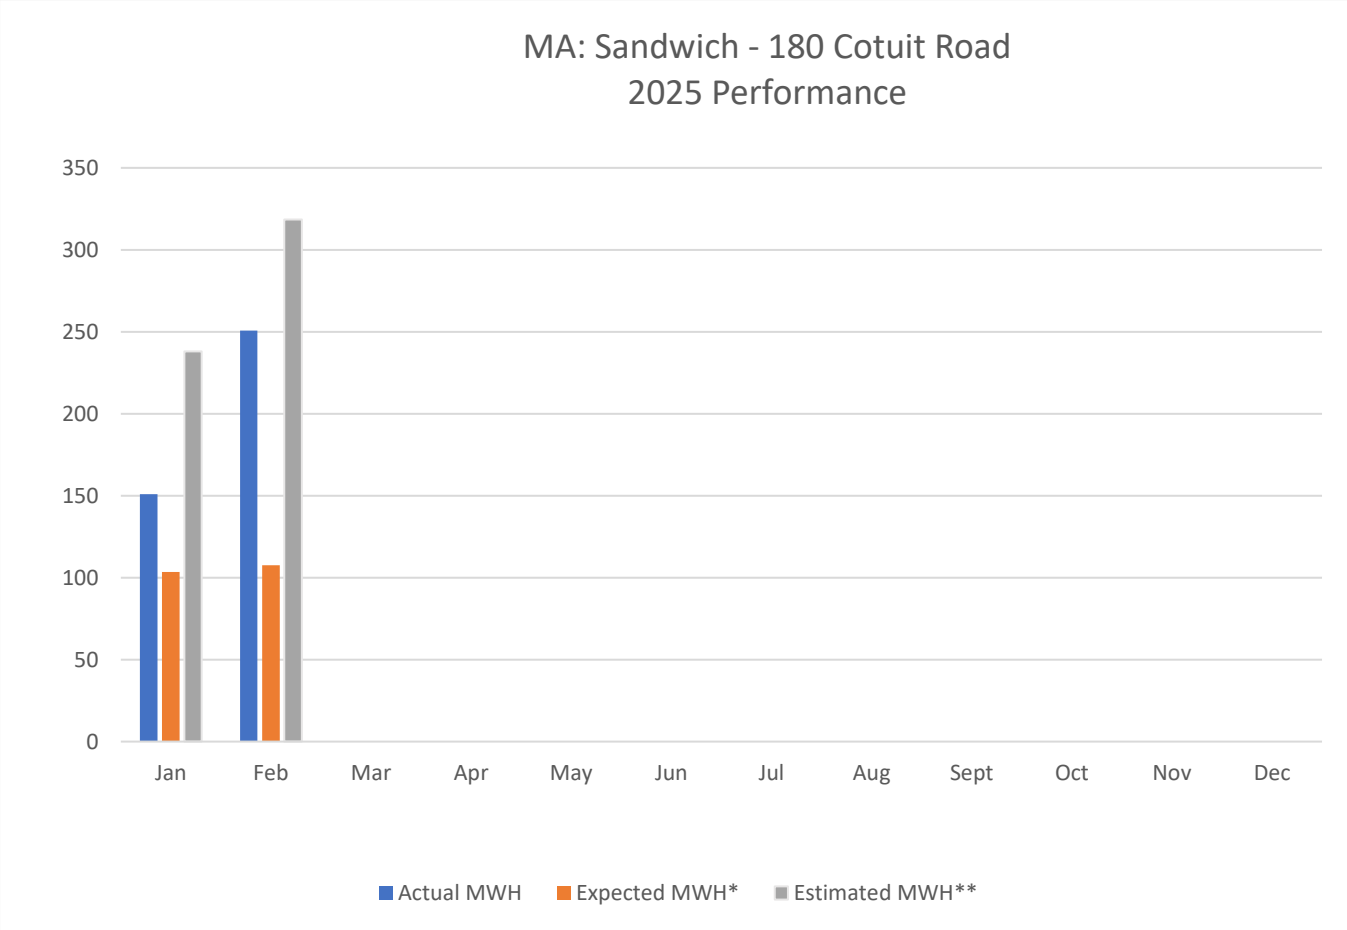

MA: Sandwich - 180 Cotuit Road Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Actual MWH	151	251										
Exp MWH*	104	108										
Est MWH**	238	318										
Act vs Exp	146%	233%										
Act vs Est	63%	79%										

Actual Performance in February 2025 was 233% of the Expected, Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 79%.

MA: Sandwich - 180 Cotuit Road January Production

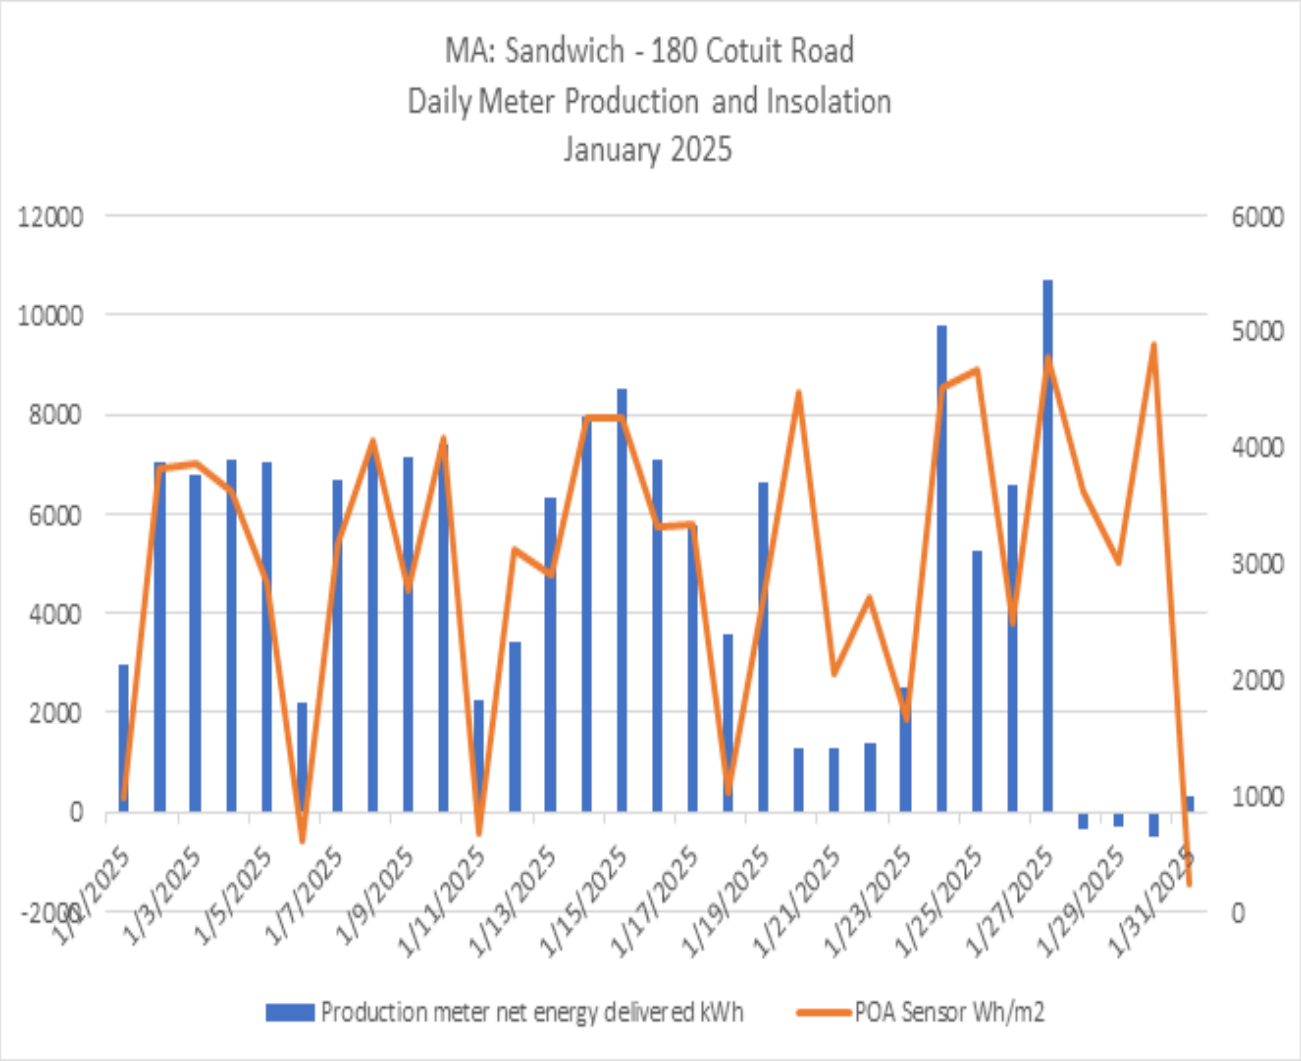

Events: -

1. The site was offline from 01/28 due to an inverter fault. Later, Power Electronics brought the site back online on 01/31 by pulling the logs. SR096048

MA: Sandwich - 180 Cotuit Road February Production

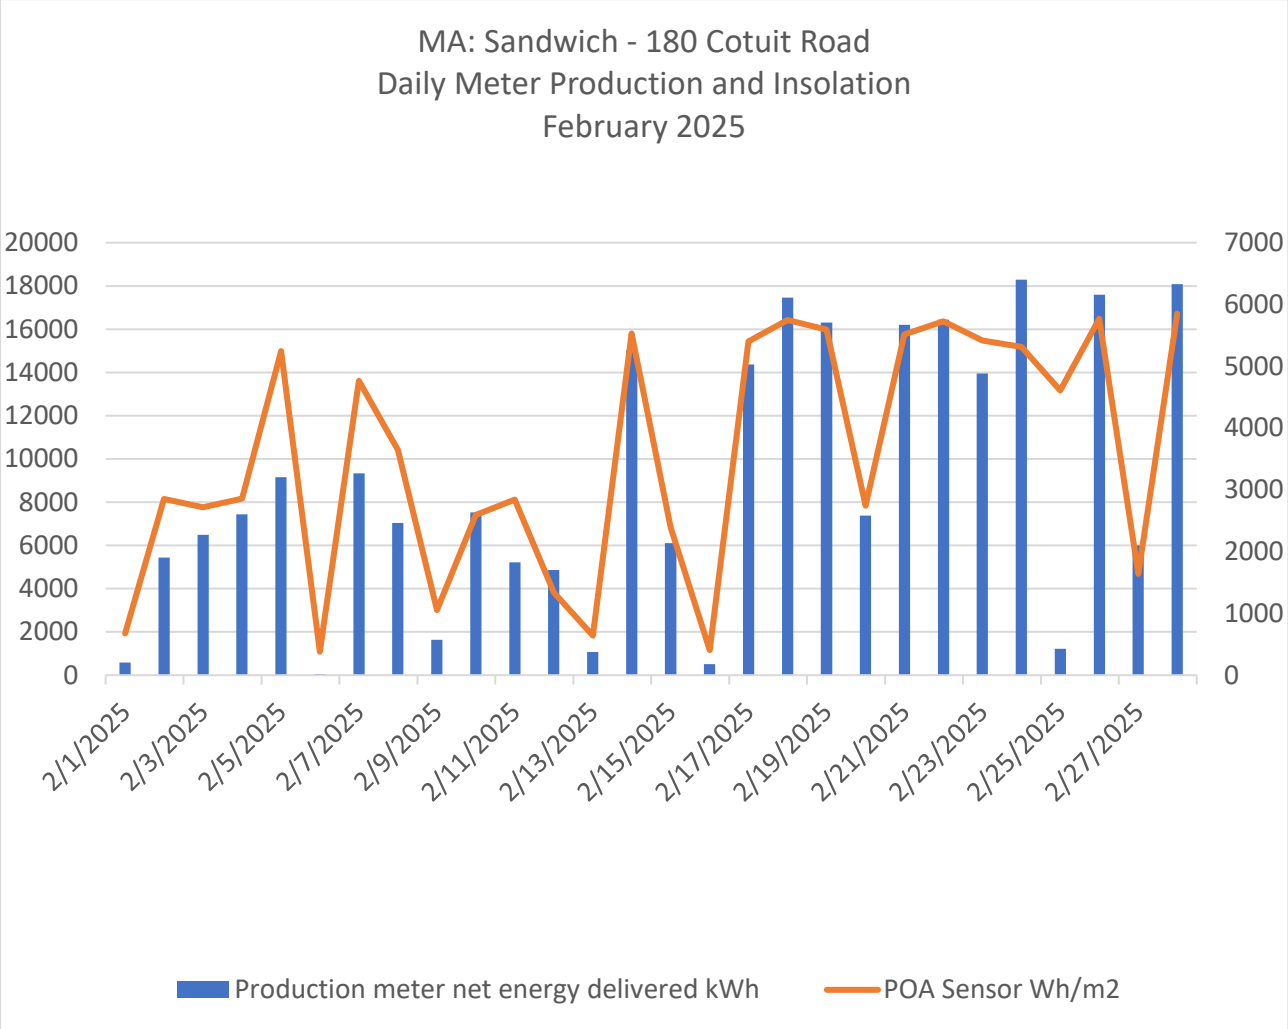

Events:

1. On 02/18/25, the technician found CB 15 strings 19 & 20 carrying 4 amps. Further investigation is needed to check for a ground fault or module issue. SR096077, SR097256.
2. The site was offline from 6:30 to 14:15 on 02/25/25 due to an inverter fault. The PE technician enabled all modules, put them in start mode, and brought the site back online. SR097746.

MA: Sandwich - 180 Cotuit Road Insolation

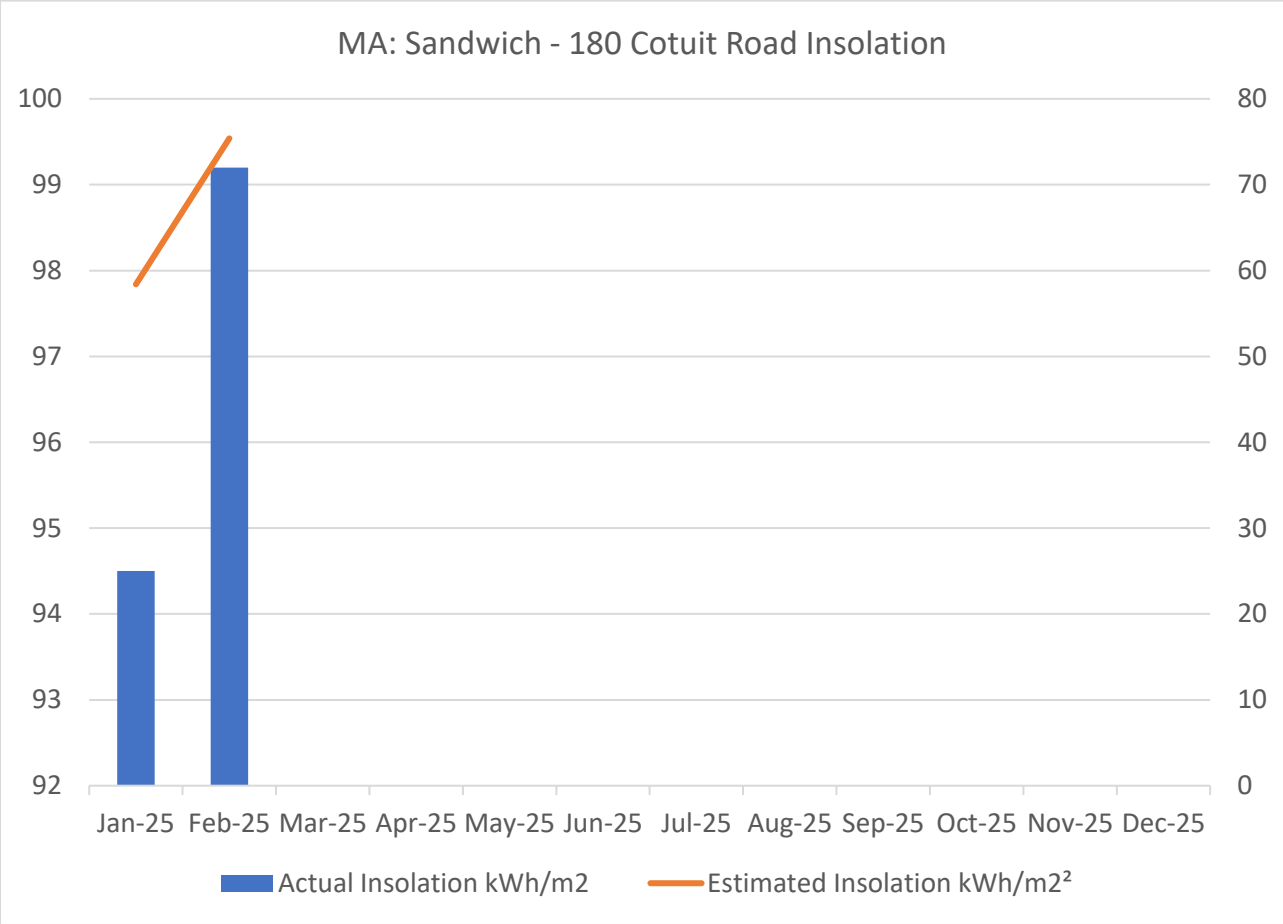

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Actual	95	99										
Est	58	75										
Act vs Est	162%	132%										

Estimated Insolation = Also Energy Estimated Insolation
