MA: Wilbraham- Three Rivers Solar Performance report

2025

System Overview

Name: Wilbraham- Three Rivers Solar
Location: Wilbraham, MA
Size AC: 4000 kWp
Size DC: 4644 kWp
Period: Feb 1, 2025 - Feb 28, 2025
Report Date: 03/11/25

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Wilbraham- Three Rivers Solar Performance

	Q1	Q2	Q3	Q4	YTD
Actual Production MWH	505				505
Expected Energy MWH*	906				906
Estimated Production MWH**	664				664
Actual vs Expected	56%				56%
Actual vs Estimated	76%				76%

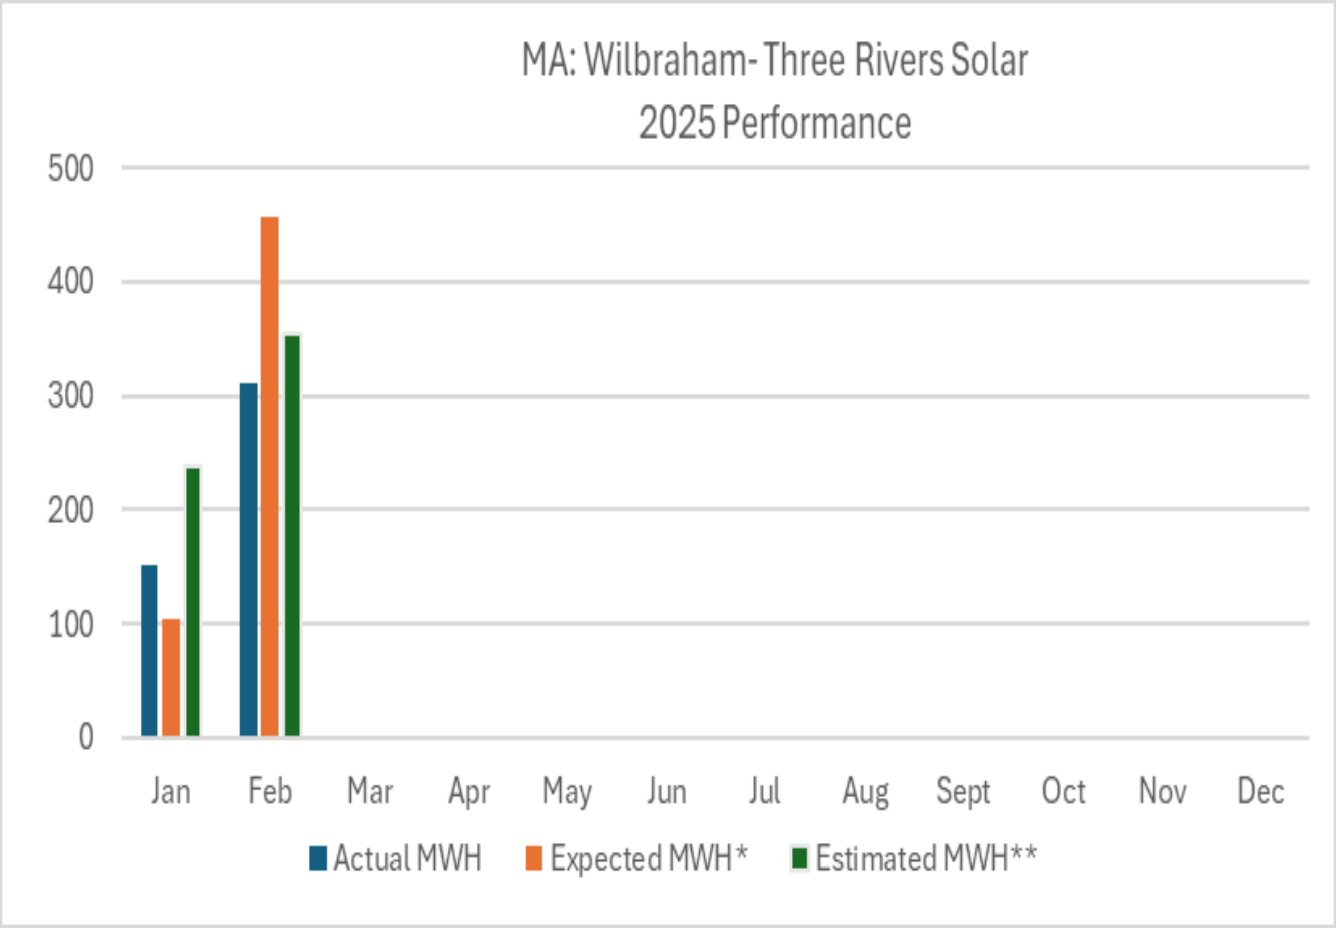

MA Wilbraham- Three Rivers Solar Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Actual MWH	194	310										
Exp MWH*	449	457										
Est MWH**	310	354										
Act vs Exp	43%	68%										
Act vs Est	63%	88%										

Actual Performance in February of 2025 was 68% of the Expected, Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 88%.

MA: Wilbraham- Three Rivers Solar January Production

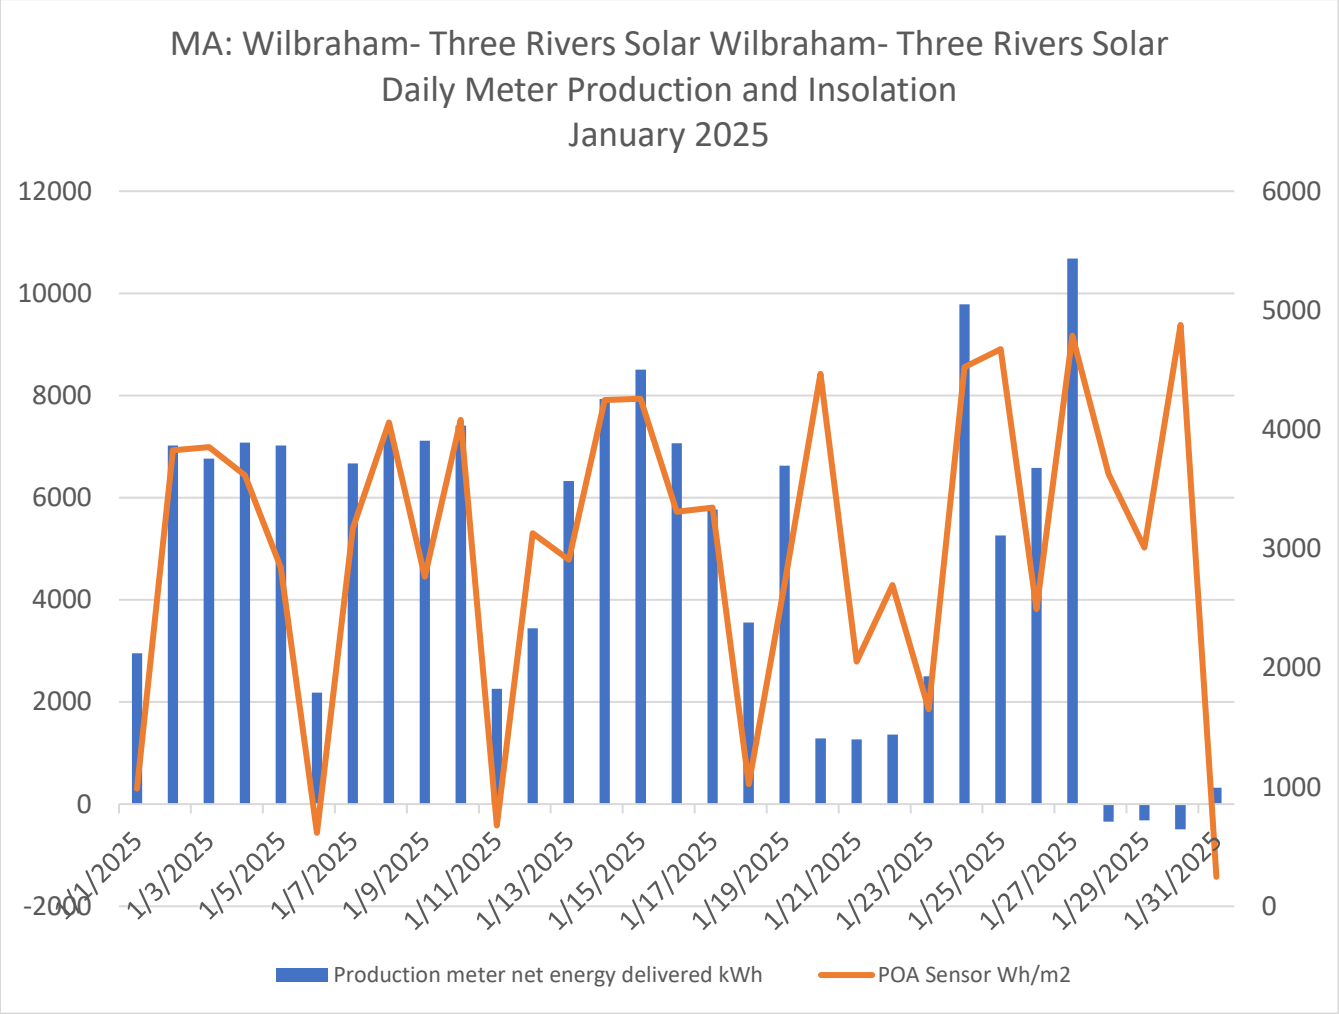

Events: -

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar February Production

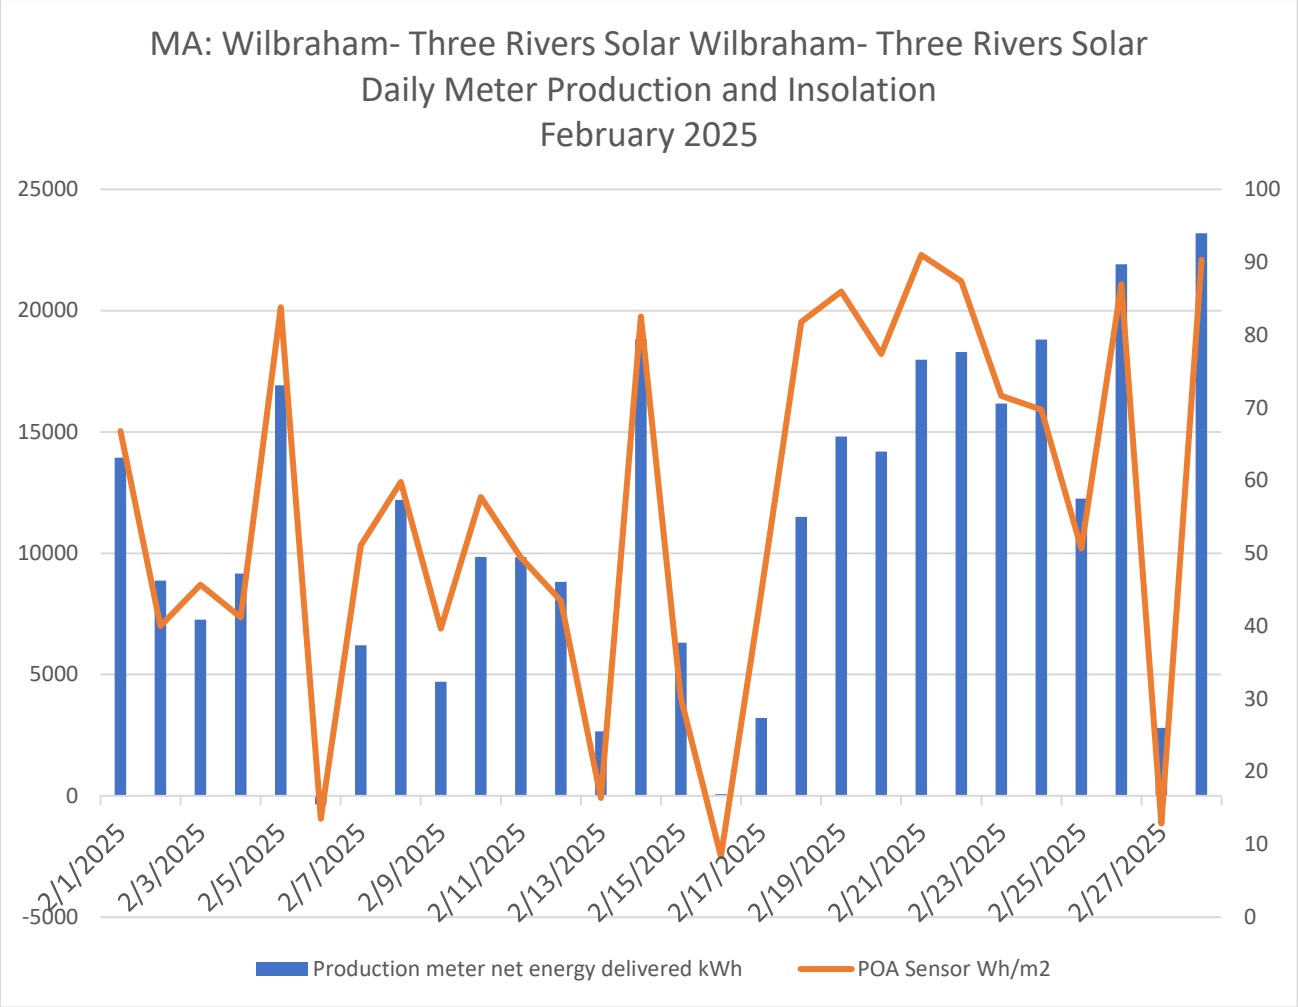

Events: -

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**
2. Site was taken offline from 12:15 to 14:00 on 02/08/25 to work on faulty modem. **SR096488, SR097054**

MA: Wilbraham- Three Rivers Solar Insolation

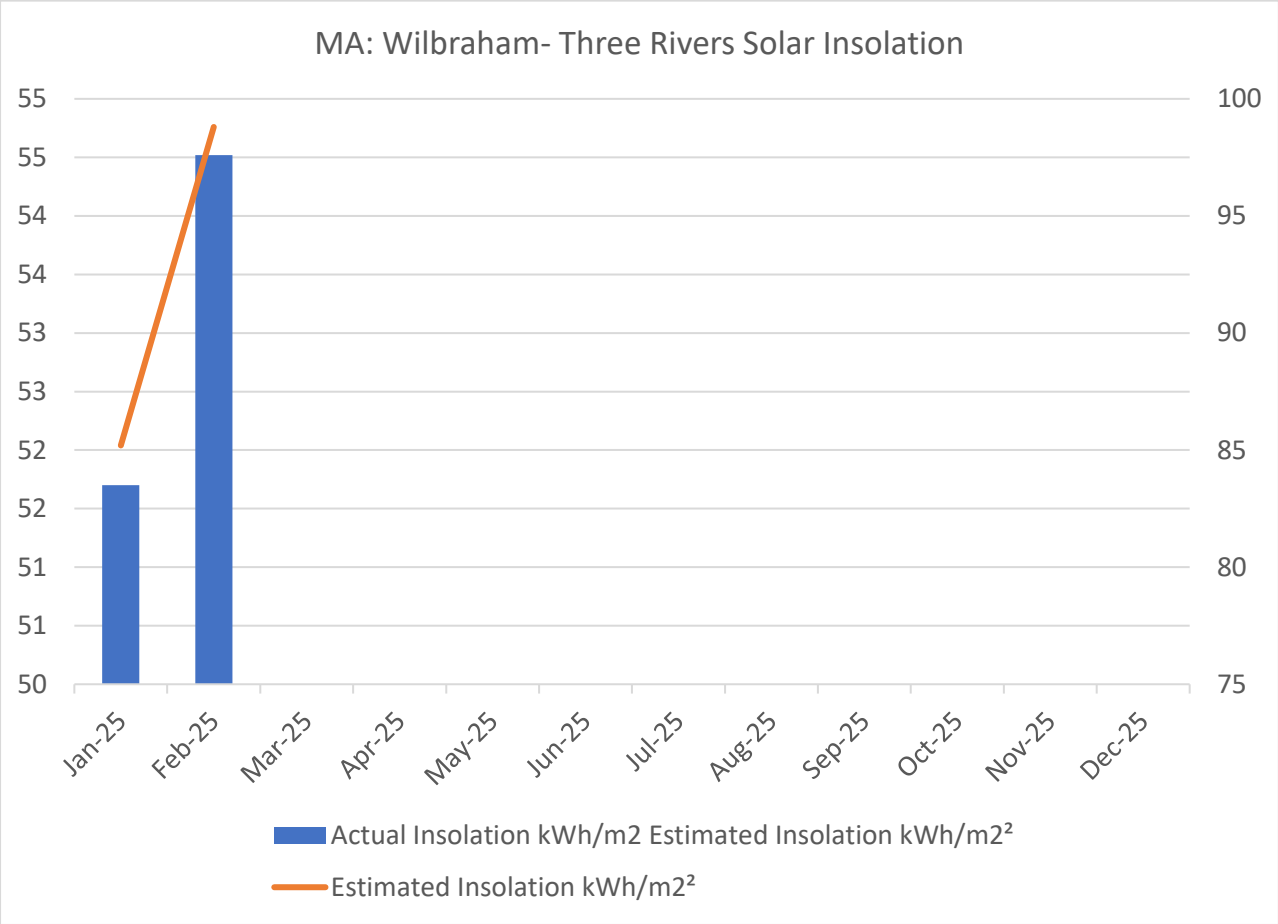

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Actual	52	55										
Estimated	85	99										
Act vs Est	61%	55%										

Estimated Insolation = Also Energy Estimated Insolation
