MA: Wilbraham- Three Rivers Solar Performance report

Q4 2025

System Overview

Name: Wilbraham- Three Rivers Solar
Location: Wilbraham, MA
Size AC: 4000 kW
Size DC: 4644kWp
Period: October 1, 2025 – October 31, 2025,
Report Date: 11/06/25

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Wilbraham- Three Rivers Solar Performance

	Q1	Q2	Q3	Q4	YTD
Actual Production MWH	1013	1706	2001	451	5171
Expected Energy MWH*	1490	1894	2085	483	5952
Estimated Production MWH**	1154	1857	1792	407	5209
Actual vs Expected	68%	90%	96%	93%	87%
Actual vs Estimated	88%	92%	112%	111%	99%

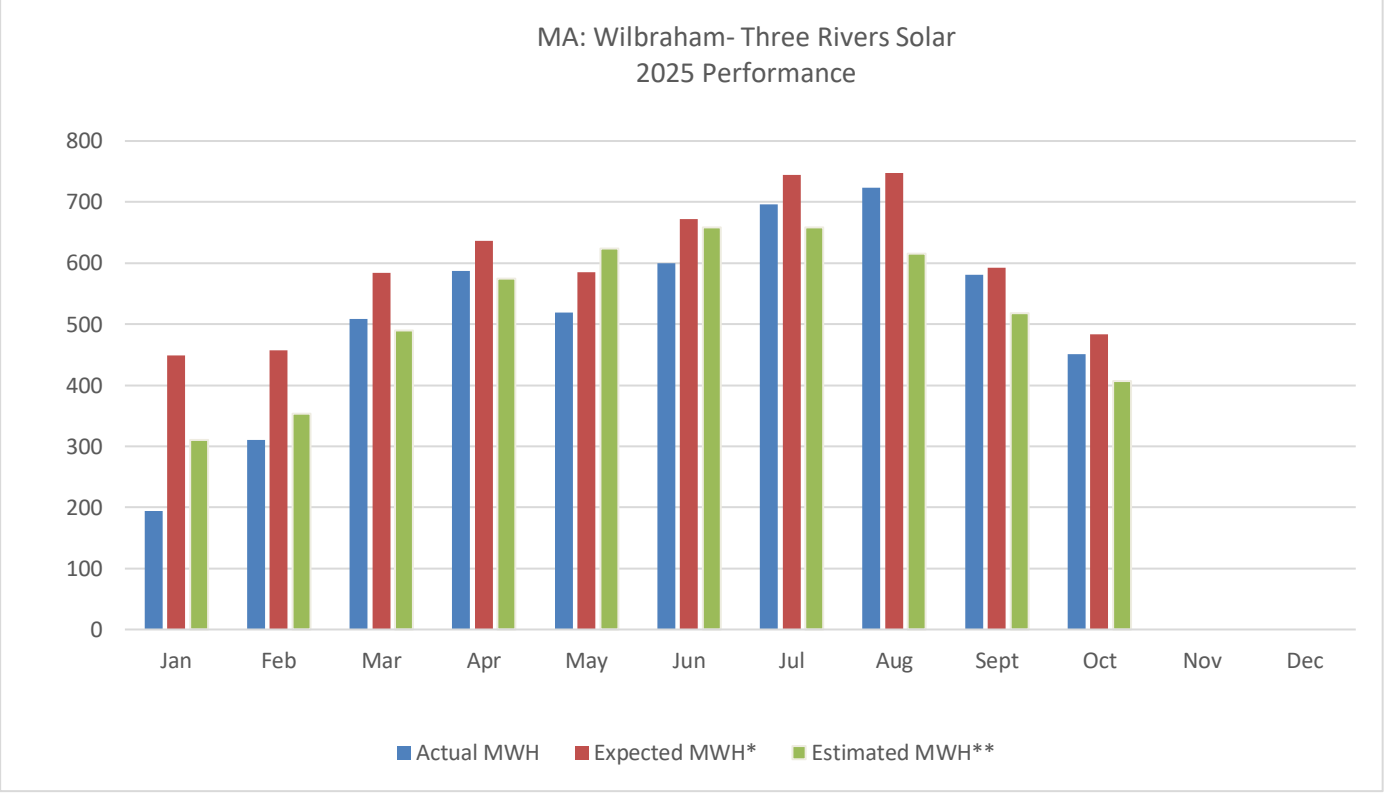

MA Wilbraham- Three Rivers Solar Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Act MWH	194	310	509	587	519	600	696	724	581	451		
Exp MWH*	449	457	584	637	585	672	744	748	593	483		
Est MWH**	310	354	490	575	624	658	659	615	518	407		
Act vs Exp	43%	68%	87%	92%	89%	89%	94%	97%	98%	93%		
Act vs Est	63%	88%	104%	102%	83%	91%	106%	118%	112%	111%		

Actual Performance in October of 2025 was 93% of the Expected Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 111%.

MA: Wilbraham- Three Rivers Solar January Production

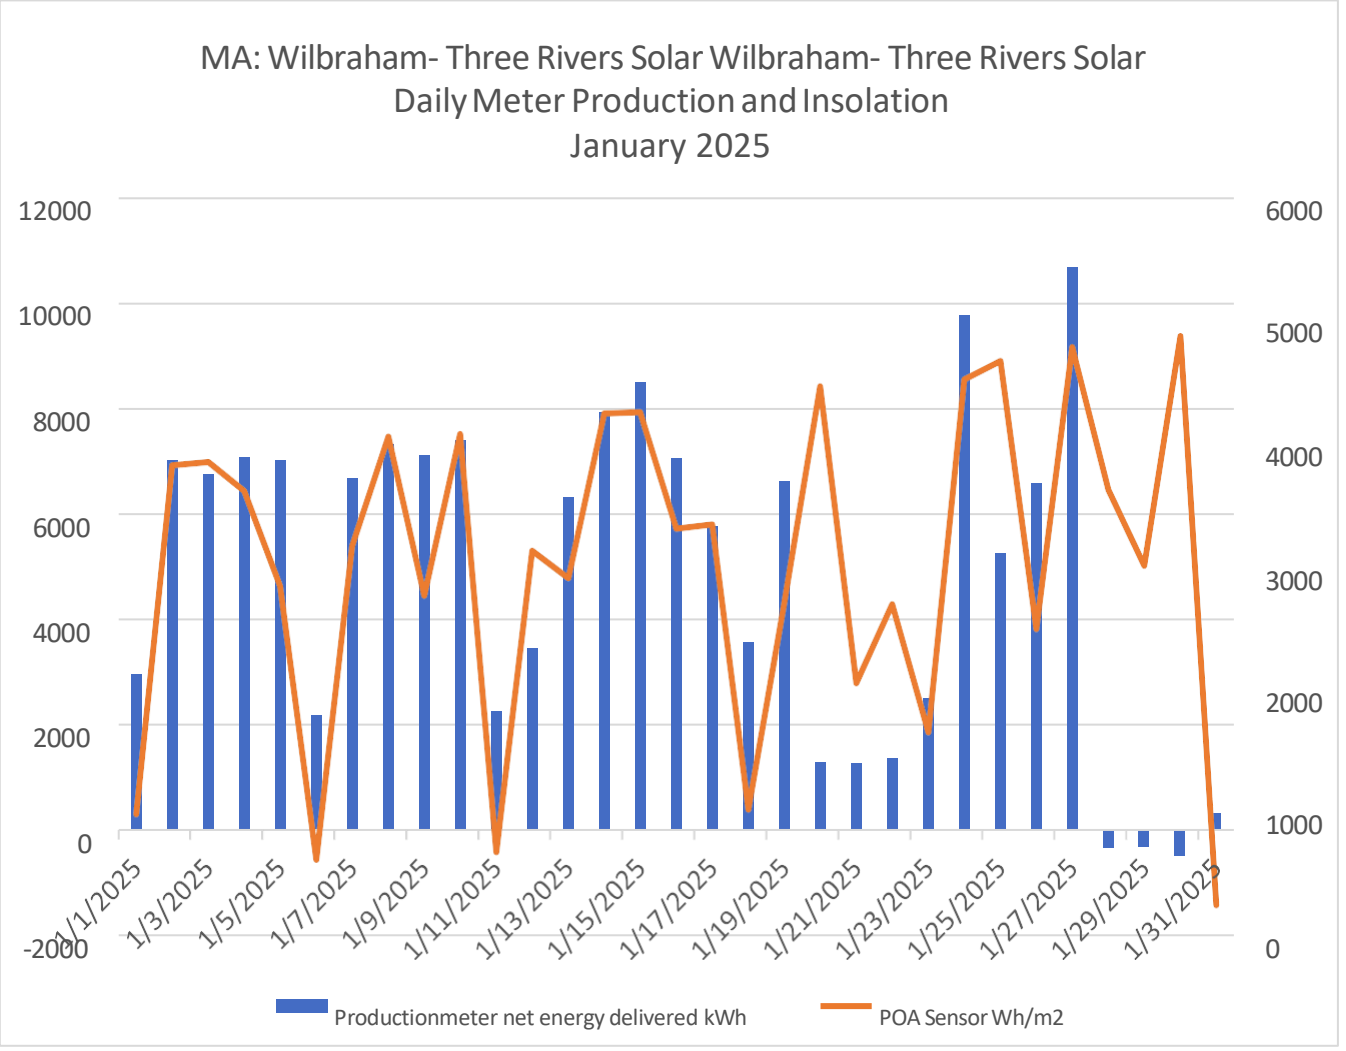

Events: -

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar February Production

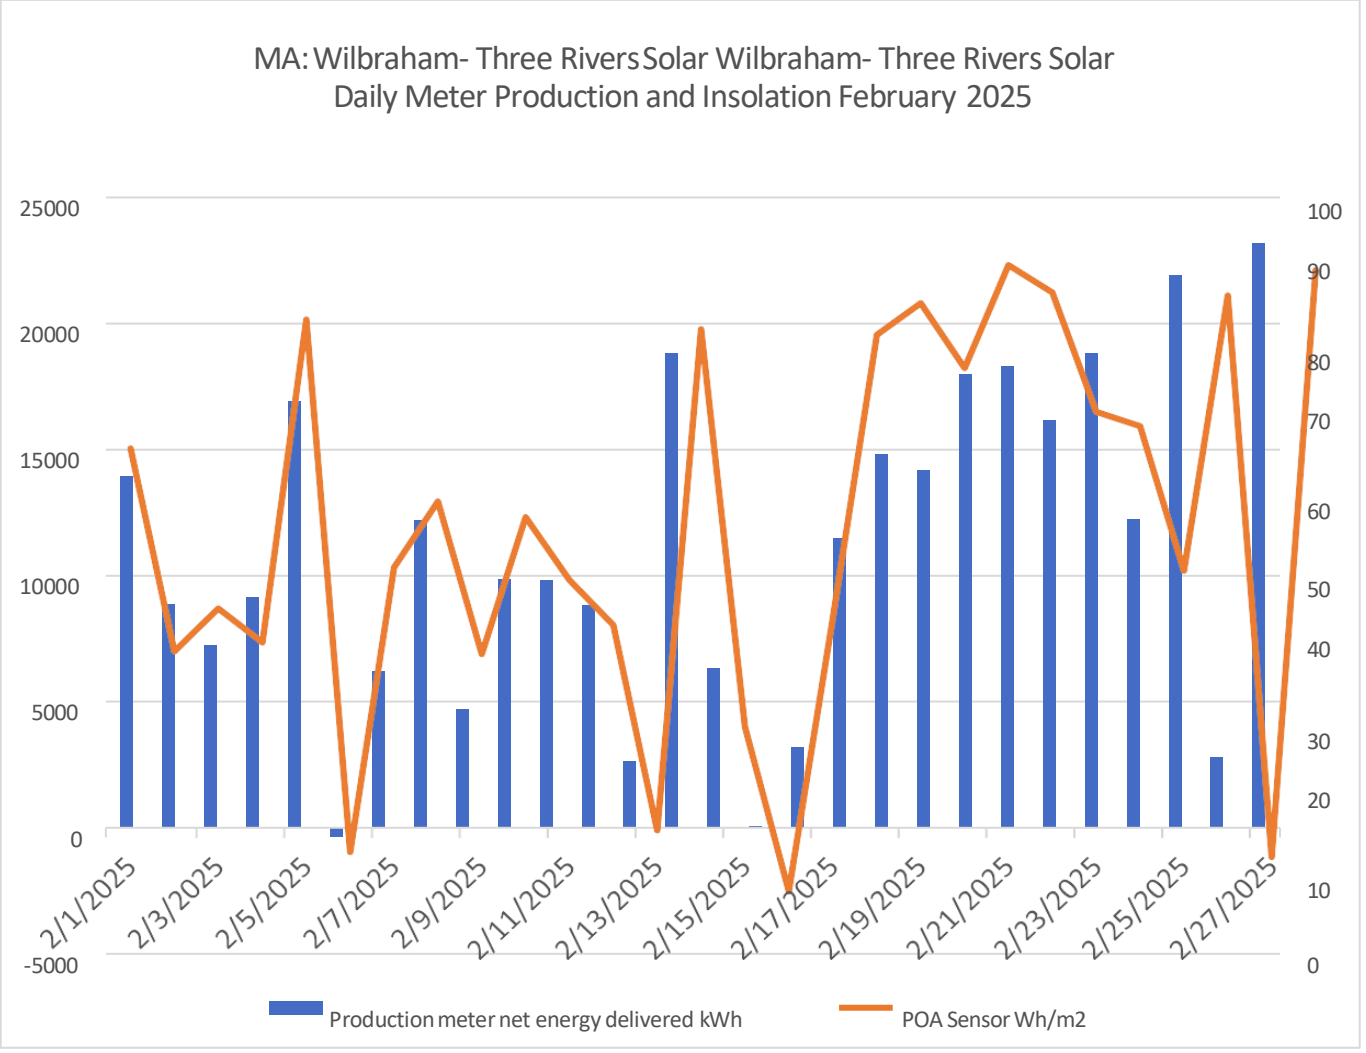

Events: -

1. The combiner boxes are notconfigured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**
2. Sitewas taken offline from 12:15 to 14:00 on 02/08/25 to work on faulty modem. **SR096488, SR097054**

MA: Wilbraham- Three Rivers Solar March Production

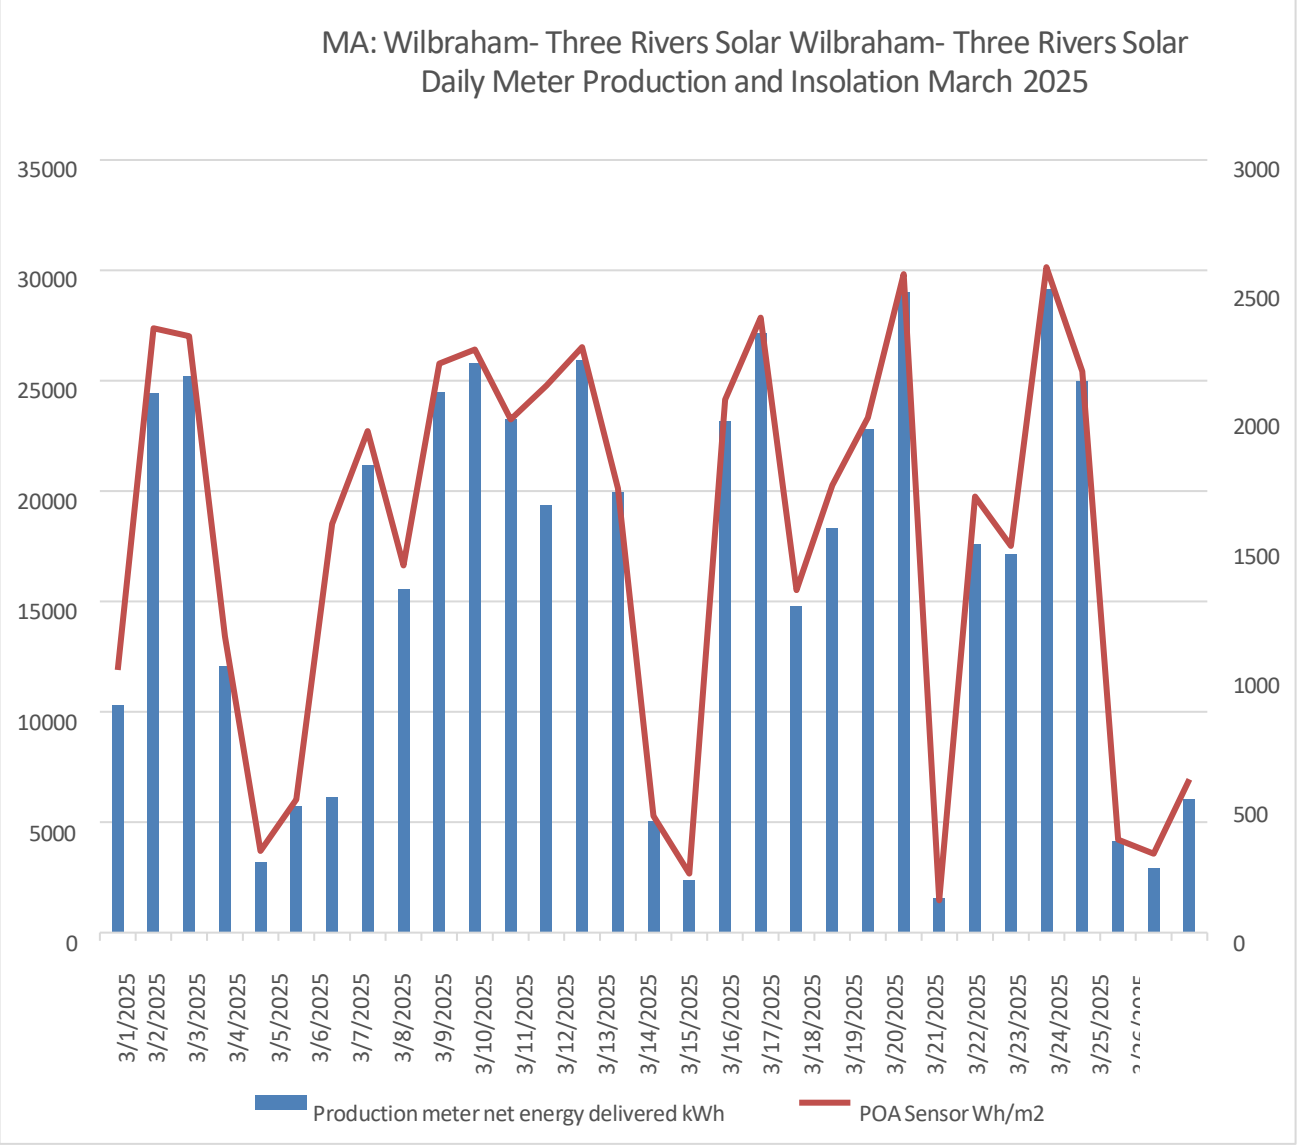

Events: -

1. Inverter 1 was offline from 11:30 to 12:45 on 03/07. The technician found a possible phantom fault due to moisture in CB22, which was dried. Inverter 1 was back online at 19:45 on 03/07. Inverter 7 was offline again from 14:05 to 15:30 on 03/13**.SR098249**
2. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar April Production

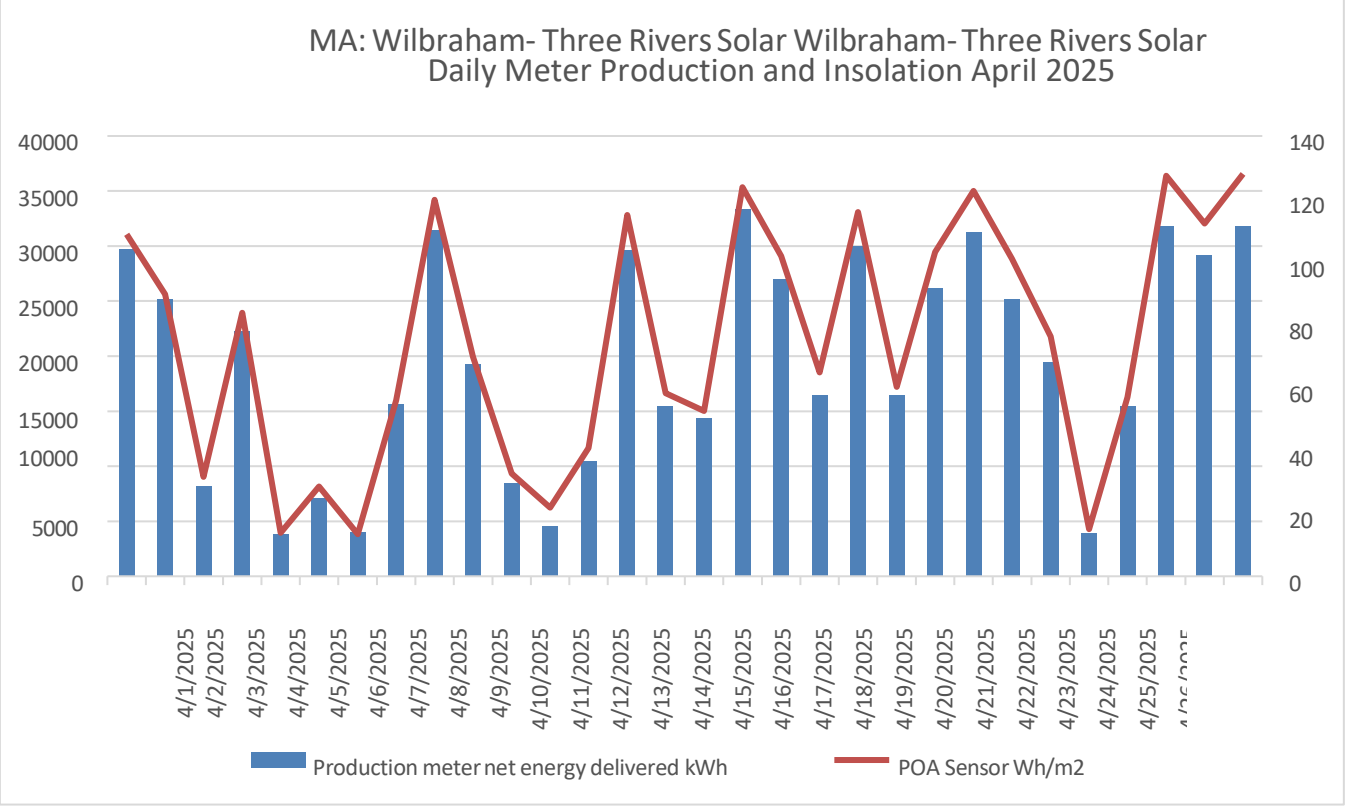

Events :-

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar May Production

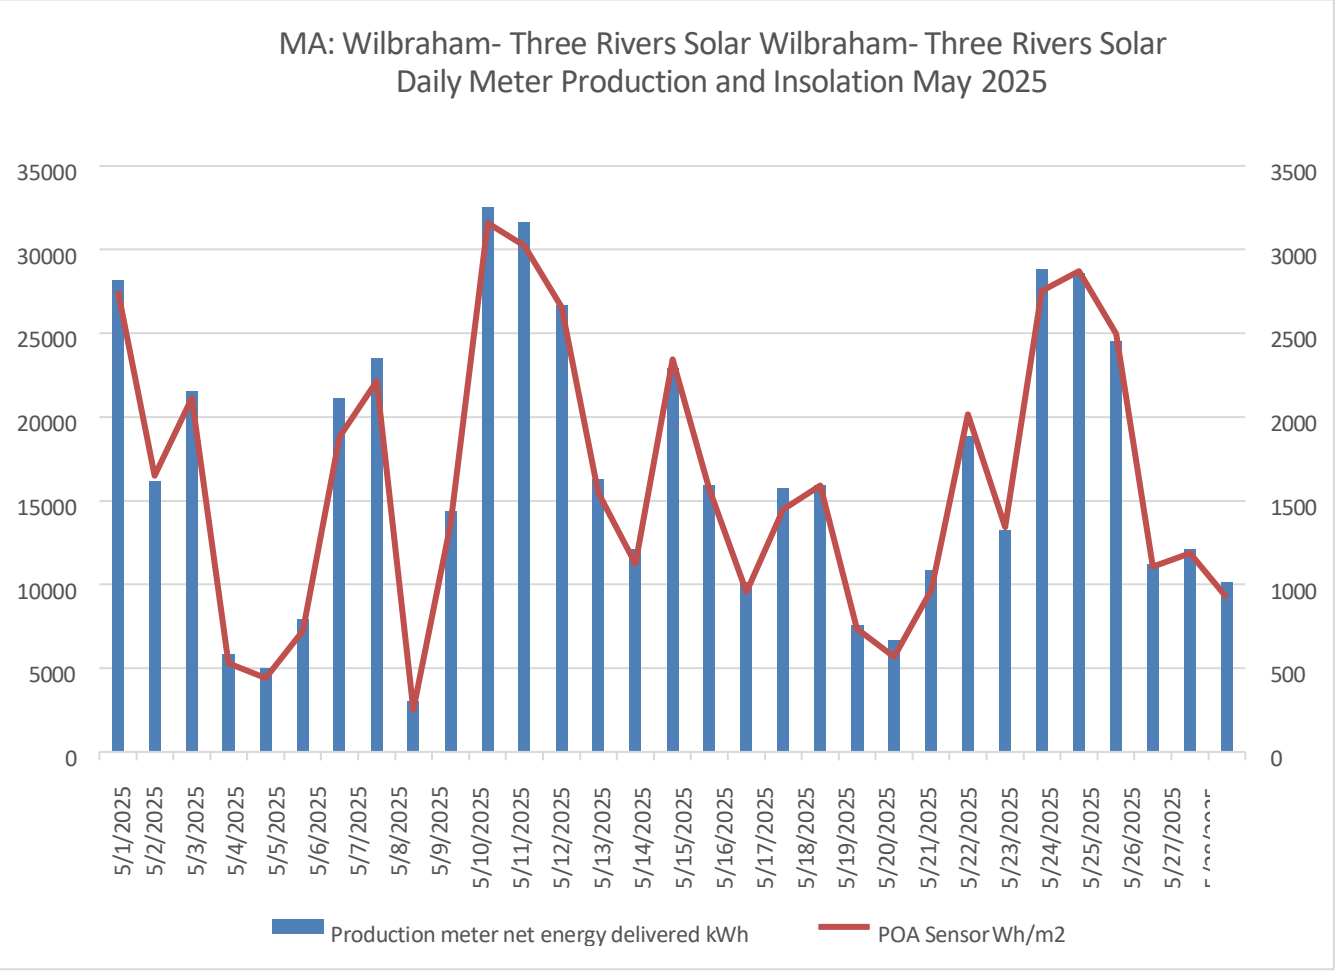

Events :-

1. The site was offline from 16:00 on 05/03 and back online at 11:15 on 05/04 after the technician re-energized the breaker. SR100974
2. Since 05/24, the inverter has been starting up around 08:00 instead of the usual 06:30, despite sufficient irradiance for DC startup. Without visibility into BESS data, it appears the inverter is either charging the BESS or being held offline by SCADA until 08:00. And requested insight from Powin Support. **SR102043, SR101891**
3. The combiner boxes are not configured properly. We are currently working in conjunction with AlsoEnergy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar June Production

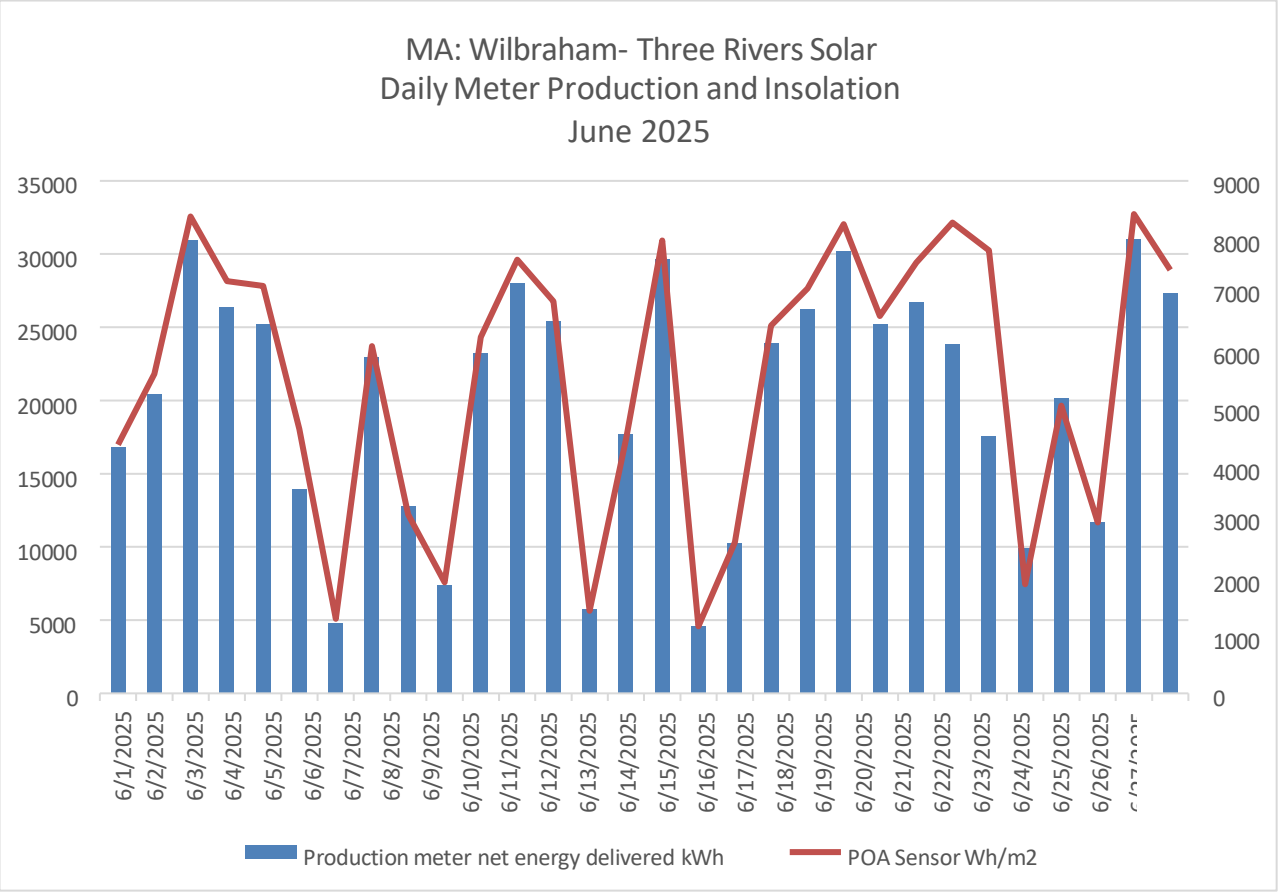

Events: -

1. The site was offline from 17:30 on 06/01 to 10:45 on 06/02. **SR102255**
2. The inverter was starting production late throughout the month. **SR101891**
3. Inverter was offline from 14:30 to 16:15 on 06/24. and again, inverter was offline from 08:30 to 11:15 on 06/25. **SR103454**

MA: Wilbraham- Three Rivers Solar July Production

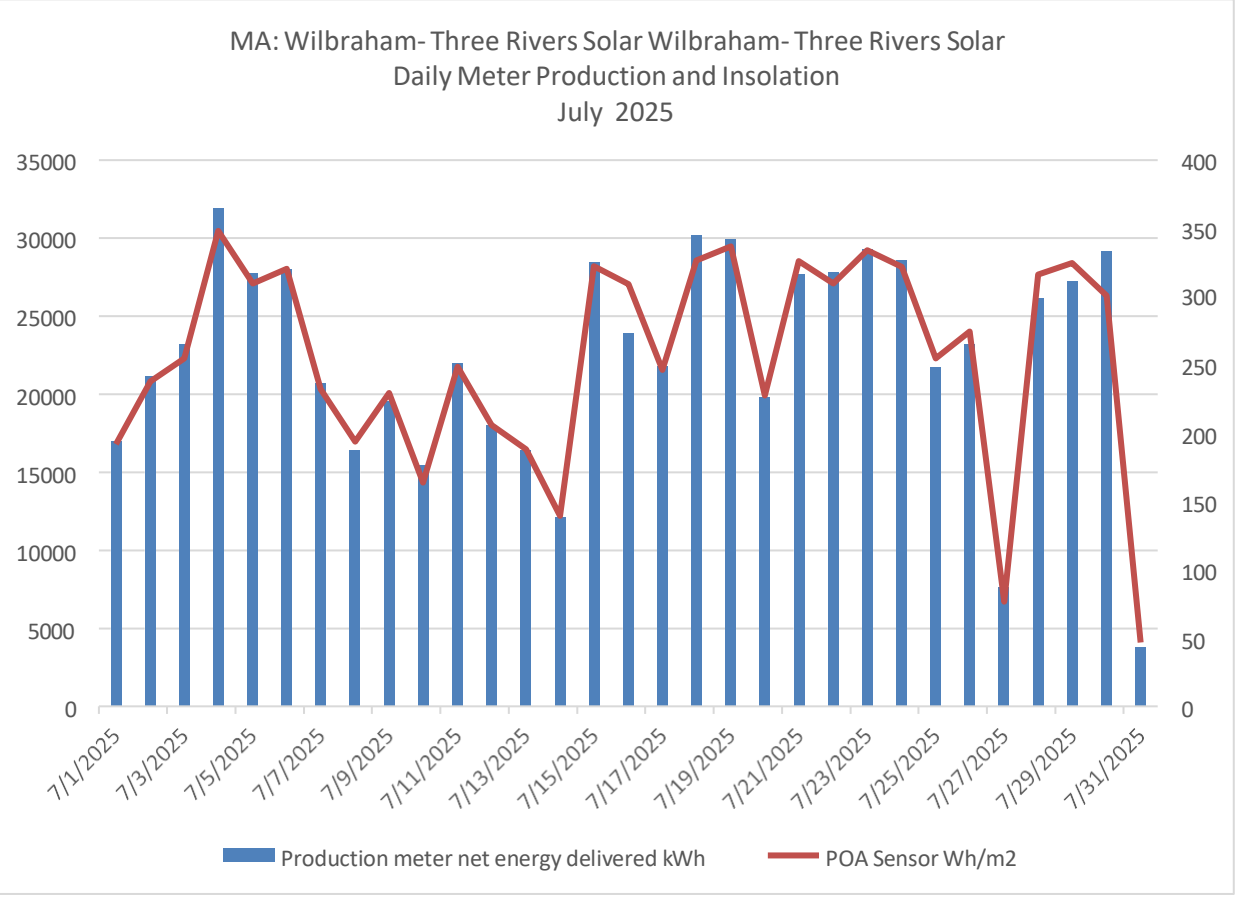

Events: -

1. Inverter was offline from 09:15 to 12:15 on 07/31. SR105424
2. Site power dropped from 10:17 to 11:15, again from 11:39 to 12:42, and once more from 16:01 to 16:58 on 07/14.

MA: Wilbraham- Three Rivers Solar August Production

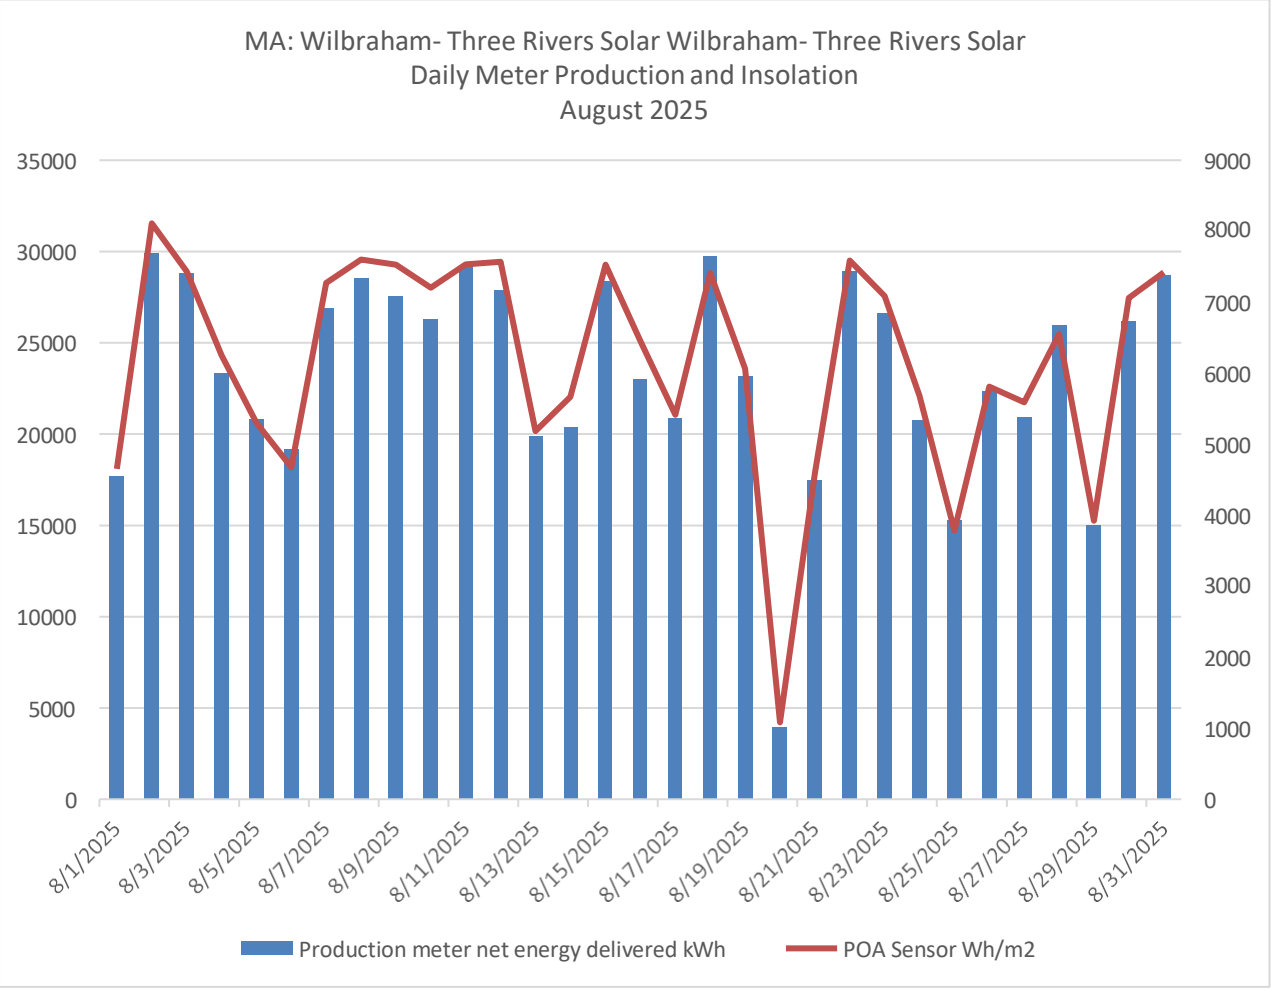

Events:-

MA: Wilbraham- Three Rivers Solar September Production

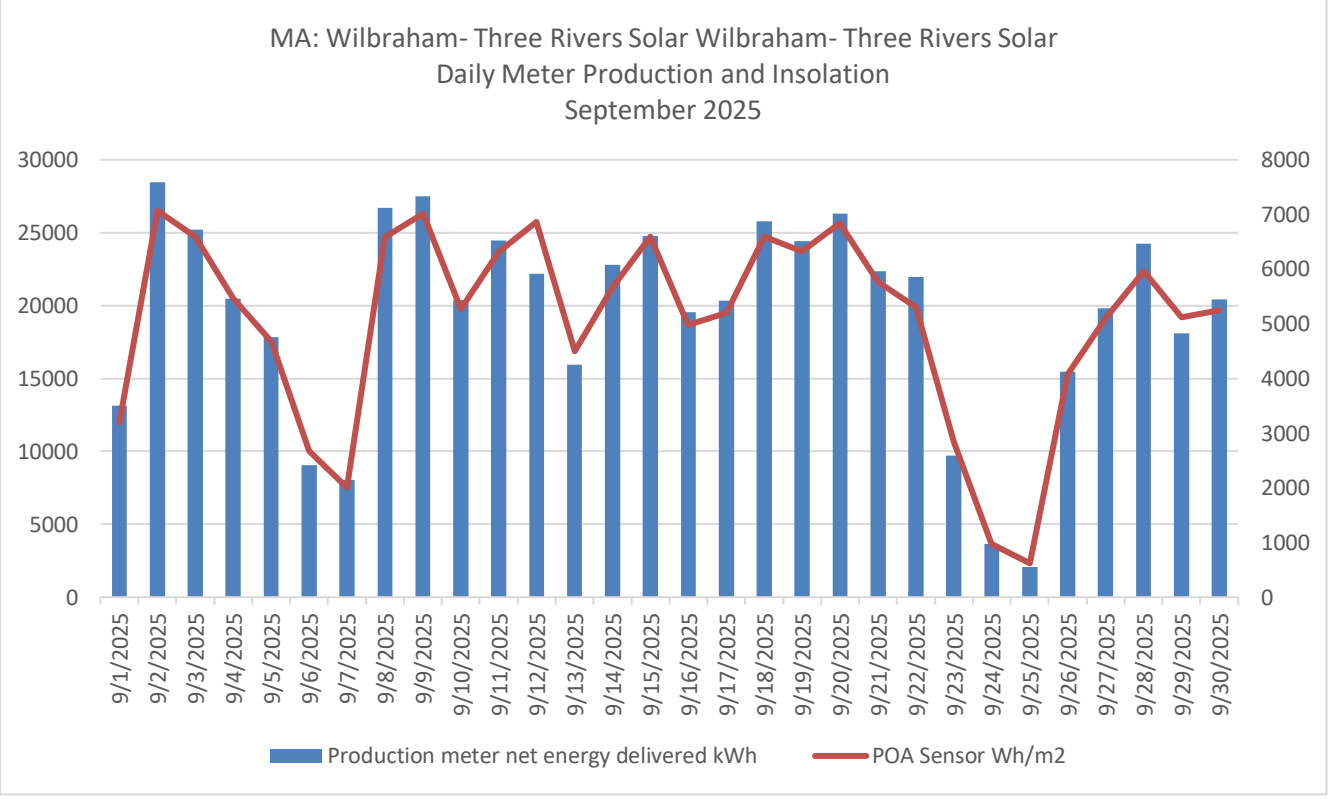

Events :-

MA: Wilbraham- Three Rivers Solar October Production

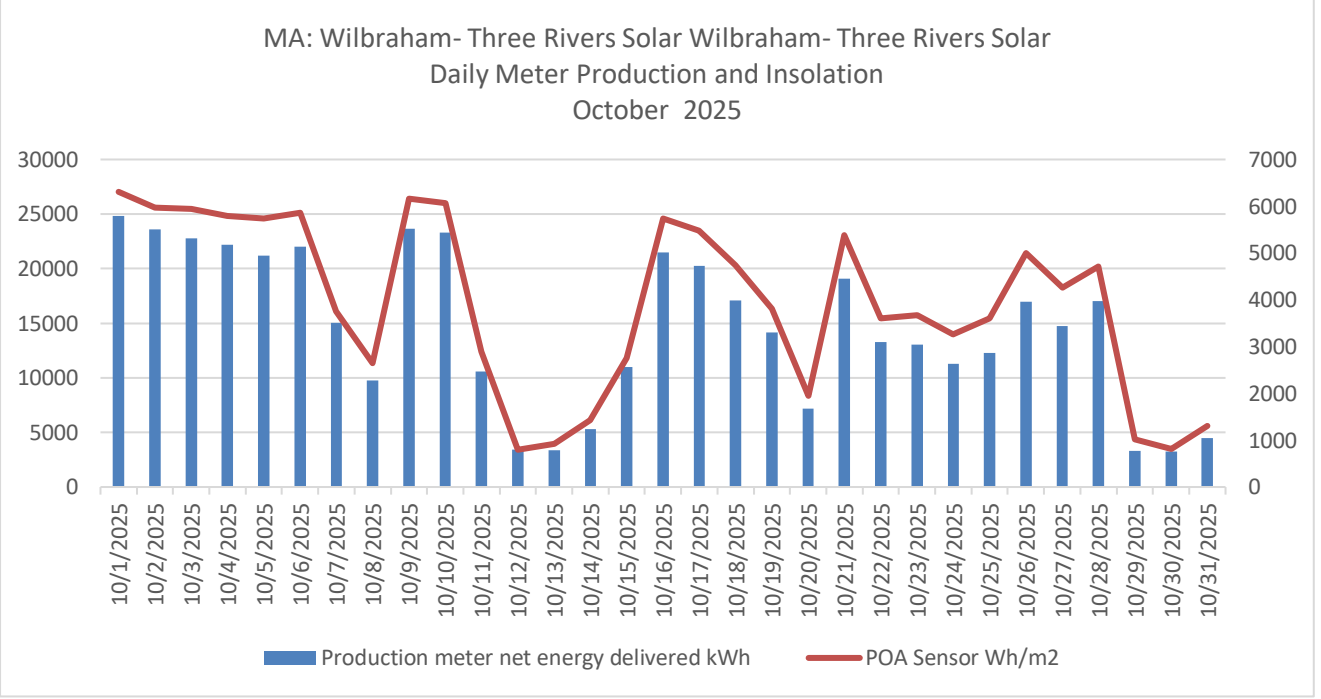

Events :-

MA: Wilbraham- Three Rivers Solar Insolation

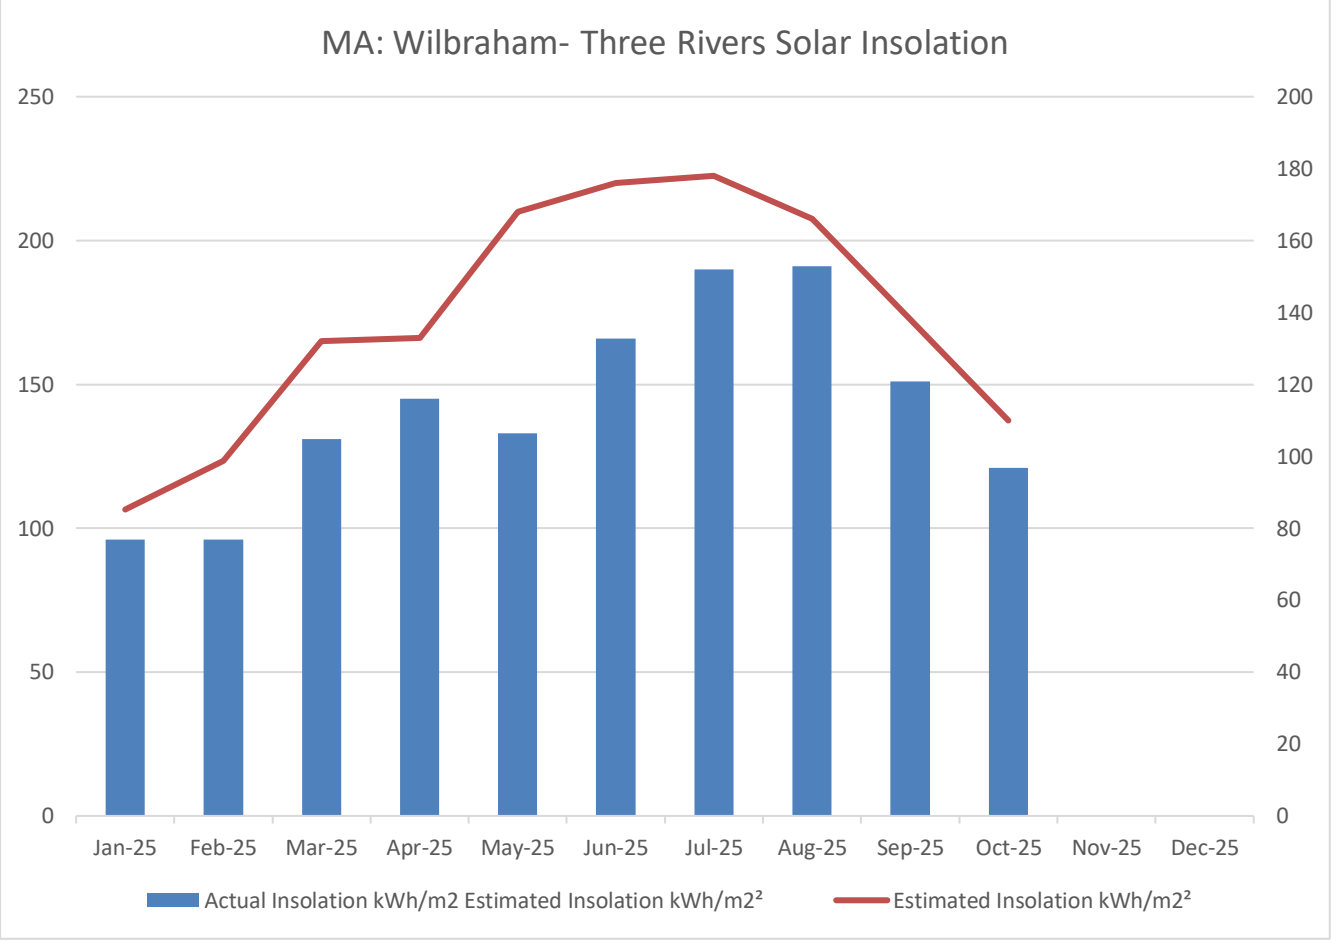

MA: Wilbraham- Three Rivers Solar Insolation

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Actual	96	96	131	145	133	166	190	191	151	121		
Est	85	99	132	151	168	176	178	166	138	110		
Act vs Est	113%	97%	99%	96%	79%	94%	107%	115%	110%	110%		

Estimated Insolation = Also Energy Estimated Insolation
