MA: Wilbraham- Three Rivers Solar Performance report

Q1 2025

System Overview

Name: Wilbraham- Three Rivers Solar
Location: Wilbraham, MA
Size AC: 4000 kW
Size DC: 4644 kWp
Period: Jan 1, 2025 – Apr 30, 2025
Report Date: 05/06/25

Prepared by:
Ameresco
117 Flanders Road, Unit 100
Westborough, MA 01581

MA: Wilbraham- Three Rivers Solar Performance

	Q1	Q2	Q3	Q4	YTD
Actual Production MWH	1013	587			1600
Expected Energy MWH*	1490	637			2127
Estimated Production MWH**	1154	575			1729
Actual vs Expected	68%	92%			75%
Actual vs Estimated	88%	102%			93%

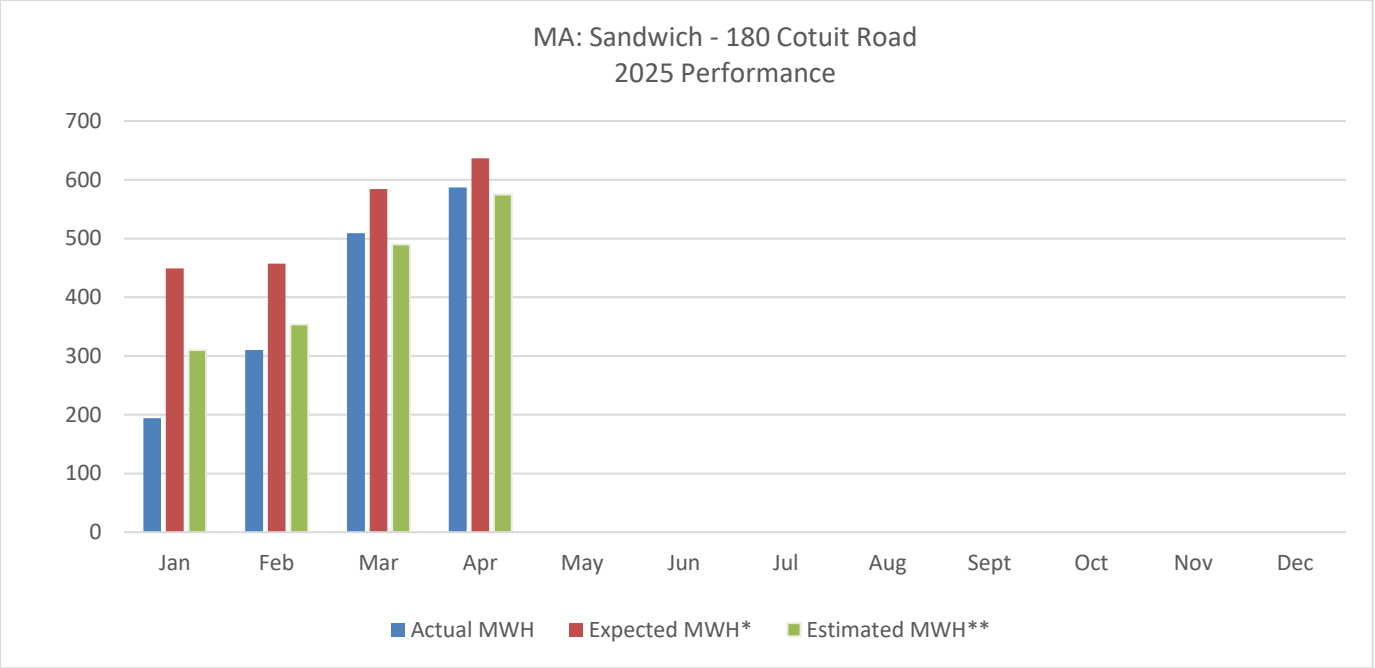

MA Wilbraham- Three Rivers Solar Monthly Performance

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec
Act MWH	194	310	509	587								
Exp MWH*	449	457	584	637								
Est MWH**	310	354	490	575								
Act vs Exp	43%	68%	87%	92%								
Act vs Est	63%	88%	104%	102%								

Actual Performance in April of 2025 was 92% of the Expected, Weather Adjusted Model, and was short of the Estimated, PVsyst Model, by 102%.

MA: Wilbraham- Three Rivers Solar January Production

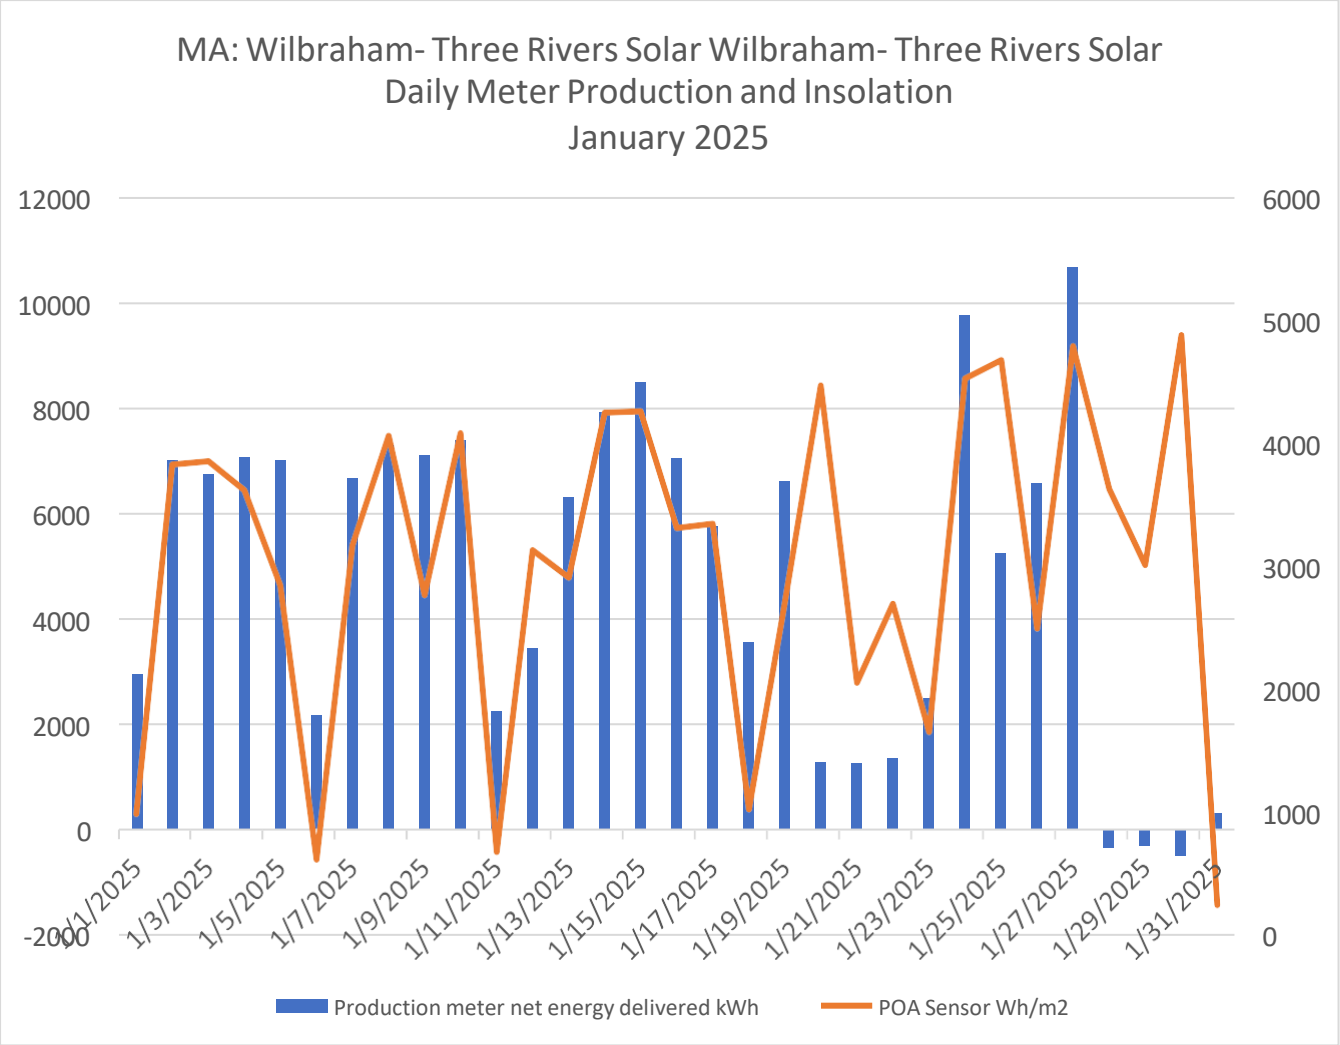

Events: -

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar February Production

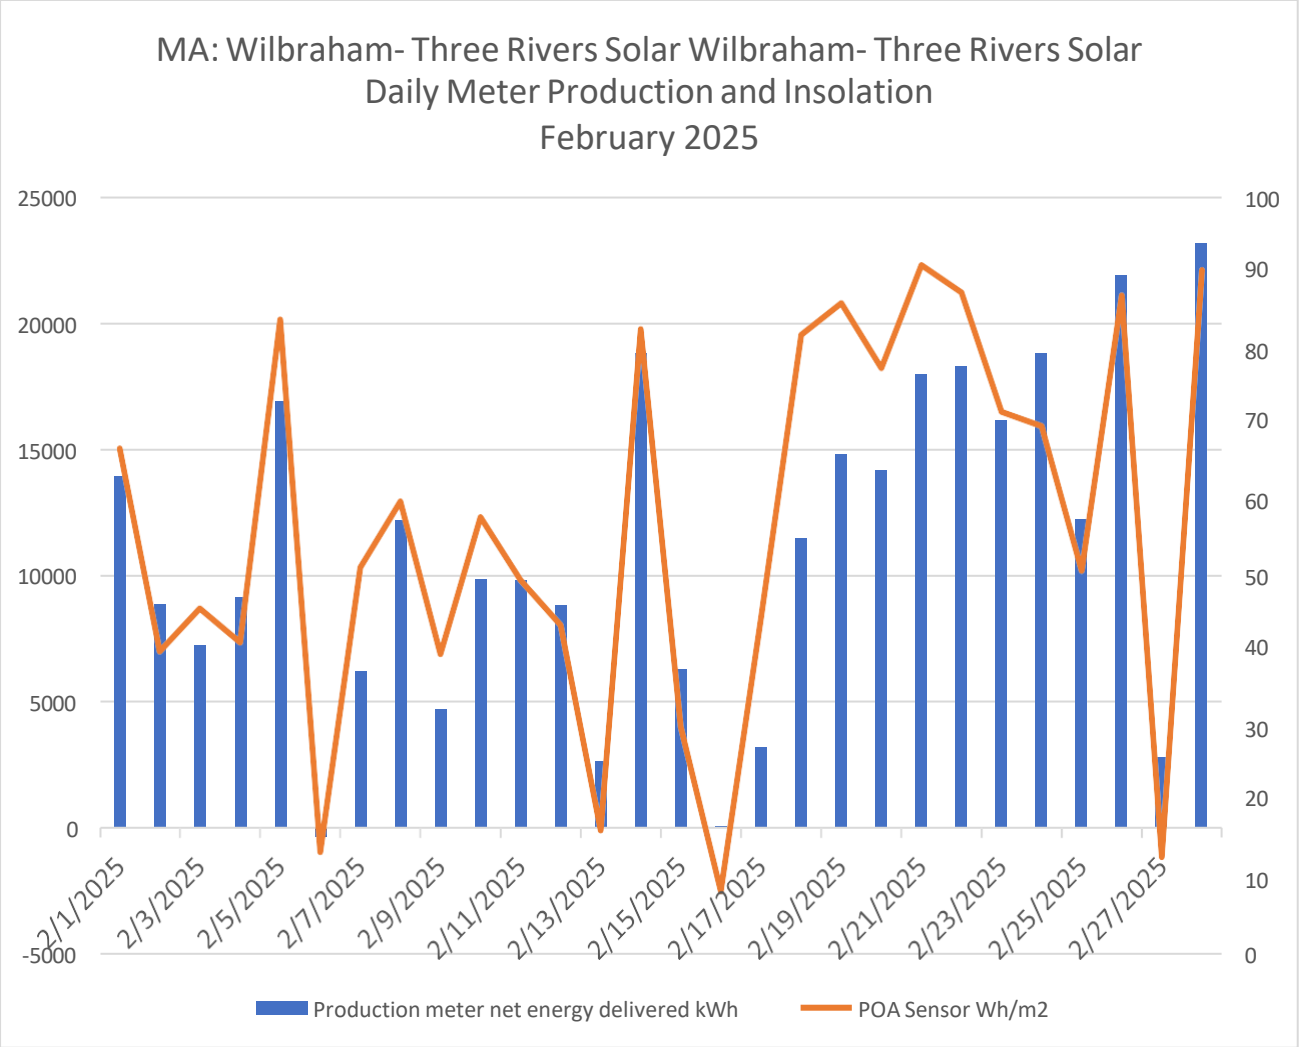

Events: -

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**
2. Site was taken offline from 12:15 to 14:00 on 02/08/25 to work on faulty modem. **SR096488, SR097054**

MA: Wilbraham- Three Rivers Solar March Production

Events: -

1. Inverter 1 was offline from 11:30 to 12:45 on 03/07. The technician found a possible phantom fault due to moisture in CB22, which was dried. Inverter 1 was back online at 19:45 on 03/07. Inverter 7 was offline again from 14:05 to 15:30 on 03/13**.SR098249**

2. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar April Production

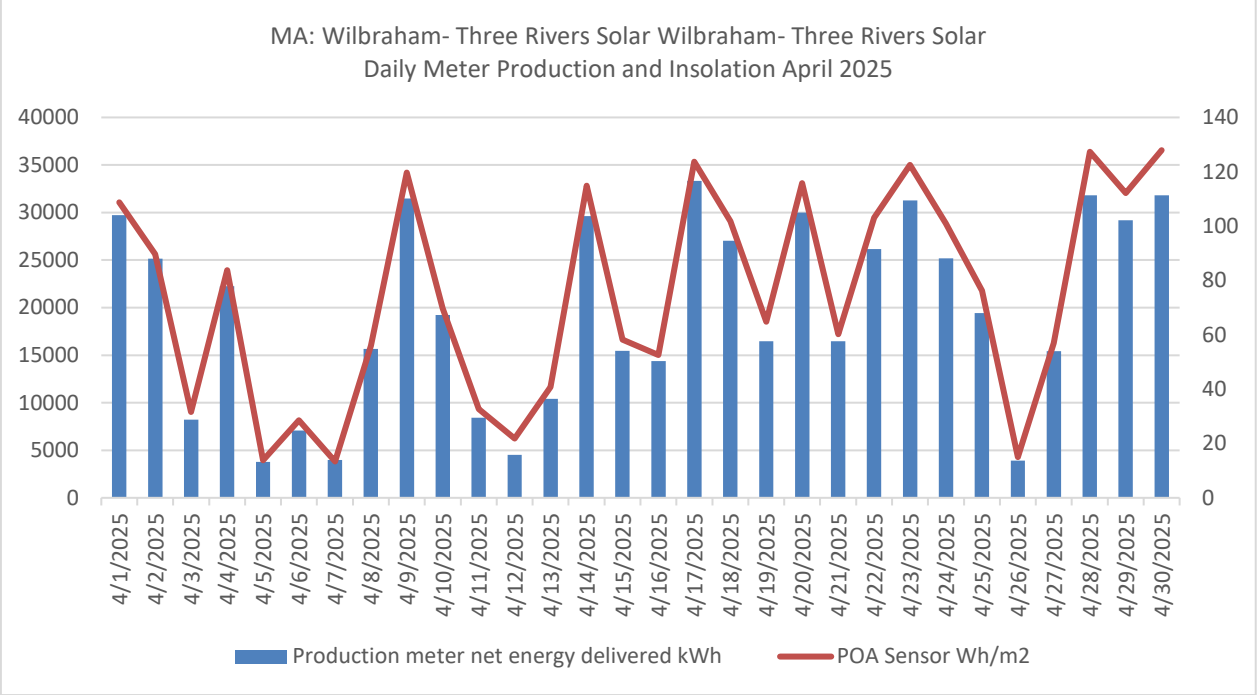

Events :-

1. The combiner boxes are not configured properly. We are currently working in conjunction with Also Energy to resolve this issue. **SR096128**

MA: Wilbraham- Three Rivers Solar Insolation

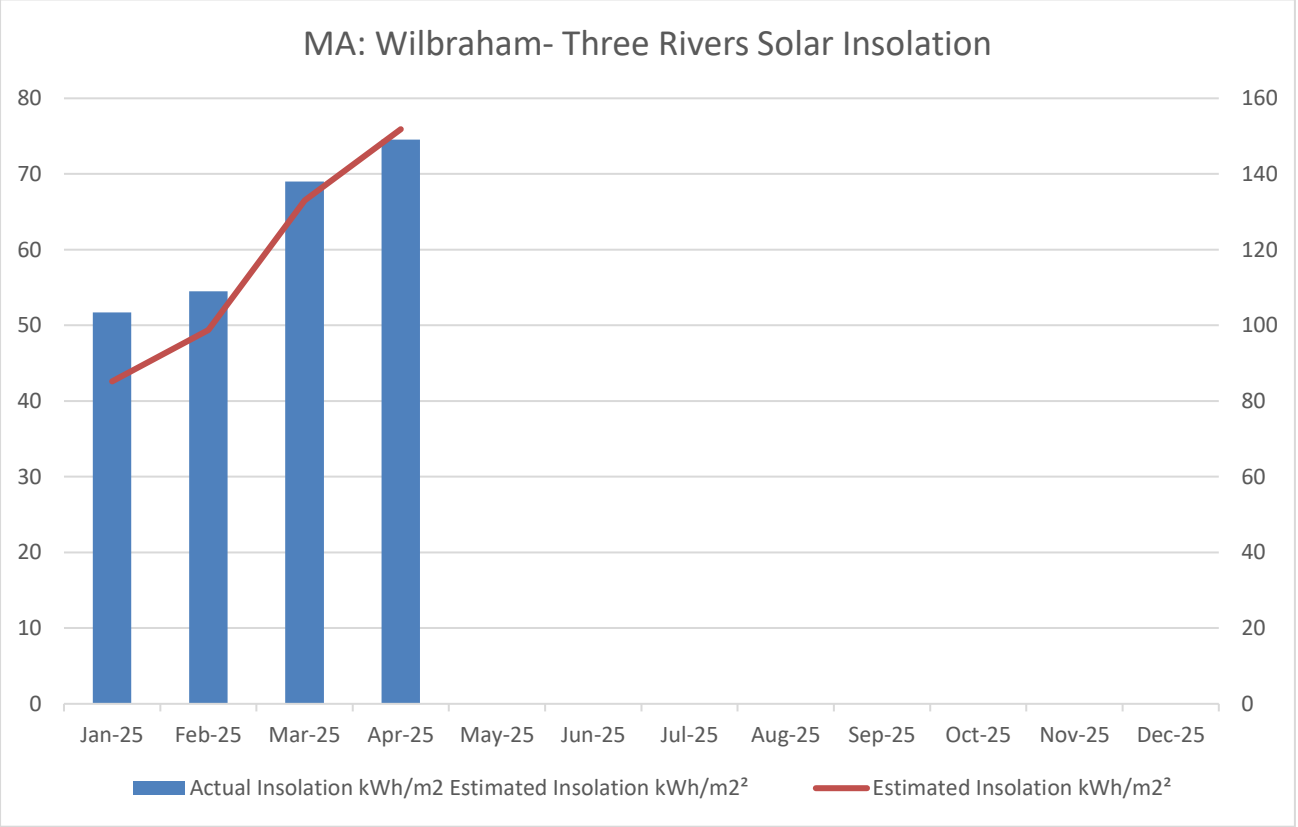

	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec
Actual	52	55	69	75								
Est	85	99	133	152								
Act vs Est	162%	56%	52%	49%								

Estimated Insolation = Also Energy Estimated Insolation
